



Selected Acquisition Report (SAR)

RCS: DD-A&T(Q&A)823-554



Multifunctional Information Distribution System (MIDS)

As of FY 2017 President's Budget

Defense Acquisition Management
Information Retrieval
(DAMIR)

Table of Contents

Common Acronyms and Abbreviations for MDAP Programs	3
Program Information	5
Responsible Office	5
References	5
Mission and Description	6
Executive Summary	7
Threshold Breaches	10
Schedule	11
Performance	14
Track to Budget	29
Cost and Funding	34
Low Rate Initial Production	66
Foreign Military Sales	67
Nuclear Costs	69
Unit Cost	70
Cost Variance	73
Contracts	77
Deliveries and Expenditures	84
Operating and Support Cost	85

Common Acronyms and Abbreviations for MDAP Programs

Acq O&M - Acquisition-Related Operations and Maintenance
ACAT - Acquisition Category
ADM - Acquisition Decision Memorandum
APB - Acquisition Program Baseline
APPN - Appropriation
APUC - Average Procurement Unit Cost
\$B - Billions of Dollars
BA - Budget Authority/Budget Activity
Blk - Block
BY - Base Year
CAPE - Cost Assessment and Program Evaluation
CARD - Cost Analysis Requirements Description
CDD - Capability Development Document
CLIN - Contract Line Item Number
CPD - Capability Production Document
CY - Calendar Year
DAB - Defense Acquisition Board
DAE - Defense Acquisition Executive
DAMIR - Defense Acquisition Management Information Retrieval
DoD - Department of Defense
DSN - Defense Switched Network
EMD - Engineering and Manufacturing Development
EVM - Earned Value Management
FOC - Full Operational Capability
FMS - Foreign Military Sales
FRP - Full Rate Production
FY - Fiscal Year
FYDP - Future Years Defense Program
ICE - Independent Cost Estimate
IOC - Initial Operational Capability
Inc - Increment
JROC - Joint Requirements Oversight Council
\$K - Thousands of Dollars
KPP - Key Performance Parameter
LRIP - Low Rate Initial Production
\$M - Millions of Dollars
MDA - Milestone Decision Authority
MDAP - Major Defense Acquisition Program
MILCON - Military Construction
N/A - Not Applicable
O&M - Operations and Maintenance
ORD - Operational Requirements Document
OSD - Office of the Secretary of Defense
O&S - Operating and Support
PAUC - Program Acquisition Unit Cost

PB - President's Budget
PE - Program Element
PEO - Program Executive Officer
PM - Program Manager
POE - Program Office Estimate
RDT&E - Research, Development, Test, and Evaluation
SAR - Selected Acquisition Report
SCP - Service Cost Position
TBD - To Be Determined
TY - Then Year
UCR - Unit Cost Reporting
U.S. - United States
USD(AT&L) - Under Secretary of Defense (Acquisition, Technology and Logistics)

Program Information

Program Name

Multifunctional Information Distribution System (MIDS)

DoD Component

Navy

Joint Participants

Air Force; Army

Navy is the lead Component as specified in the Under Secretary of Defense for Acquisition, Technology, and Logistics (USD (AT&L)) Navy Program Delegation Decisions Acquisition Decision Memorandum (ADM) dated July 24, 2012

Responsible Office

CAPT Robert Croxson
MIDS Program Office
33050 Nixie Way
Bldg 17A, Suite 422
San Diego, CA 92147-5416

Phone: 619-524-1549
Fax: 619-524-1639
DSN Phone: 524-1549
DSN Fax: 524-1639
Date Assigned: May 19, 2015

robert.d.croxson@navy.mil

References

SAR Baseline (Production Estimate)

Navy Acquisition Executive (NAE) Approved Acquisition Program Baseline (APB) dated March 22, 2006

Approved APB

Assistant Secretary of the Navy (Research, Development & Acquisition) (ASN(RDA)) Approved Acquisition Program Baseline (APB) dated November 12, 2013

Mission and Description

The Multifunctional Information Distribution System (MIDS) program consists of two products, MIDS Low Volume Terminal (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS).

The MIDS-LVT is the product of the MIDS International Program Office (IPO), a multinational (U.S., France (FRA), Germany (DEU), Italy (ITA), and Spain (ESP)) cooperative development program with joint service participation (U.S. Navy (USN), U.S. Army (USA), and U.S. Air Force (USAF)). The DoD established the program to design, develop and deliver low volume, lightweight tactical information system terminals for U.S. and Allied fighter aircraft, bombers, helicopters, ships, and ground sites. MIDS-LVT provides interoperability with North Atlantic Treaty Organization (NATO) and non-NATO users, significantly increasing force effectiveness and minimizing hostile actions and friend-on-friend engagements. Three principal configurations of the terminal are in production and use an open system, modular architecture. MIDS-LVT (1) includes voice, Tactical Air Navigation (TACAN) and variable power transmission and provides a Link 16 capability to the F/A-18, which was previously unable to use Joint Tactical Information Distribution System (JTIDS) due to space and weight limitations. MIDS-LVT(2) is an Army variant of MIDS-LVT tailored as a functional replacement for the JTIDS Class 2M terminal. MIDS-LVT(3), also referred to, as MIDS Fighter Data Link (FDL), is a reduced function terminal for the Air Force (no voice, no TACAN). MIDS-LVT contracted for Block Upgrade 2 (BU2) to incorporate Cryptographic (Crypto) Modernization (CM), Enhanced Throughput (ET), and Frequency Remapping (FR) in the MIDS-LVT terminal.

MIDS JTRS is designed as a U.S. Only Pre-Planned Product Improvement (P3I), executed as an Engineering Change Proposal (ECP) to the production MIDS-LVT configuration, and is fully compatible with MIDS-LVT. MIDS JTRS completed qualification in first quarter of FY 2010. It facilitated the Joint Program Executive Office (JPEO) JTRS incremental approach for fielding advanced JTRS transformational networking capability and transformed the MIDS-LVT into a four channel, Software Communications Architecture (SCA) compliant, Joint Tactical Radio. A form-fit-function replacement to MIDS-LVT, MIDS JTRS also adds three programmable 2 Megahertz (MHz) to 2 Gigahertz (GHz) channels capable of hosting the JTRS legacy and networking Waveforms (WFs). In addition to the Link 16, TACAN, and voice functionality found in MIDS-LVT, and MIDS-LVT BU2, MIDS JTRS adds capabilities such as CM, ET, FR, software programmability, Four Net Concurrent Multi-Netting with Concurrent Contention Receive (CMN-4), and Tactical Targeting Network Technology (TTNT). CMN-4 and TTNT are integral components of Naval Integrated Fire Control – Counter Air (NIFC-CA) and link together aircraft carrier strike group E-2Ds and EA-18s, and the aircraft carrier itself.

Executive Summary

Program Highlights Since Last Report:

The Multifunctional Information Distribution System (MIDS) Program Office (MPO) consists of two products, the MIDS Low Volume Terminal (MIDS-LVT) and the MIDS Joint Tactical Radio System (MIDS JTRS). The MIDS Program Manager (PM) continues implementation of an acquisition strategy that maintains continuous competition between the two U.S. production contractors, Datalink Solutions (DLS) and ViaSat, a software contract with BAE Systems, and directed procurements to EuroMIDS for MIDS-LVT. DLS is a consortium between BAE Systems and Rockwell Collins. EuroMIDS is a consortium among Airbus Defense & Space, Indra, Finmeccanica, and Thales.

MIDS-LVT Block Upgrade 2 (BU2) is a 39-month Engineering Change Proposal (ECP) awarded November 2013 to bring National Security Agency (NSA) mandated Crypto Modernization (CM) and National Telecommunications and Information Agency and Federal Aviation Agency mandated Frequency Remapping (FR) capability to the terminal.

MIDS-LVT is continuing development efforts and working to mitigate software integration issues and a potential schedule delay and funding shortfall. MIDS-LVT conducted multiple Hardware (HW)/Software (SW) Critical Design Reviews (CDRs) with vendors in February and March 2015 in support of the MIDS-LVT and BU2 efforts to successfully demonstrate design maturity in the areas of system, software, hardware, and security:

- DLS Hardware CDR was conducted in Wayne, NJ, on February 9-10, 2015.
- The Joint BAE, Thales, and Warner Robins Air Logistics Complex Centralized Software Support Activity (CSSA) Software CDR was held in at Wayne, NJ, on February 11-13, 2015.
- The EuroMIDS BU2 Hardware CDR was conducted in Rome, ITA, on March 4-5, 2015.
- The ViaSat Hardware CDR was held at Carlsbad, CA, on March 25-26, 2015.

The MIDS Steering Committee #54 was hosted by Germany in Berlin, on March 17-19, 2015. Key agreements were obtained on the approval of the MIDS Program Management Plan (PMP) for the MIDS International Program Office (IPO) and concurrence on financial procedures for FY 2016. The next MIDS Steering Committee #55 was held in Rome, Italy on September 22-24, 2015. The meeting was chaired by Program Executive Officer for Tactical Aircraft Programs PEO(T) and focused on the status of the cooperative development of MIDS-LVT BU2.

The MIDS International Review Board (MIRB) #23 met in Brussels, Belgium, May 4-8, 2015, with 310 participants from 29 countries to discuss North Atlantic Treaty Organization's (NATO's) integration of MIDS and MIDS-LVT BU2. MIRB #24 was held in Washington, DC on November 16-20, 2015, with 335 attendees from 28 Nations/Agencies. Topics included keynote addresses by PEO(T) and Air Force Headquarters Air Combat Command Deputy Director of Plans, Programs and Requirements, and updates on MIDS Products, Software, and Platforms.

As a follow-on to the MIDS JTRS Core terminal, MIDS JTRS Four Net Concurrent Multi-Netting with Concurrent Contention Receive (CMN-4) is being implemented as an ECP, and is considered a low risk enhancement to Link 16 while providing a significant upgraded capability for the Fleet. The MIDS Program Office (MPO) has coordinated all platform integration and test efforts with F/A-18 Program Management Air (PMA-265) throughout all MIDS efforts. This close relationship continues with the MIDS JTRS CMN-4 enhancement. Coordination involves over 3,500 hours of laboratory testing with no hardware failures, completion of the first MIDS JTRS CMN-4 flight in March 2015 and the completion of Government First Article Qualification Testing (GFAQT) in May 2015. MIDS JTRS CMN-4 Problem Reports (PRs) are being addressed as they are identified in Developmental Test (DT). Full MIDS JTRS CMN-4 functionality has been demonstrated successfully in the laboratory and inflight testing. MIDS JTRS is also enhancing the MIDS JTRS CMN-4 capability as MIDS Modernization Increments (MMI). MMI 1 development delivery orders were awarded to DLS and ViaSat in June 2015. The U.S. Air Force has also recognized the value of the MIDS JTRS CMN-4 capability and has begun development efforts to support migrating F-15, F-16 and F-22 squadrons to MIDS JTRS CMN-4.

The MIDS JTRS Tactical Targeting Network Technology (TTNT) L-Band development continued with a CDR on July 21-22, 2015. As a result of the Middle Class Tax Relief and Job Creation Act of 2012 and resulting spectrum sell-off, the MIDS

JTRS TTNT spectrum use will now include S-Band. Compensation for the sell-off and S-Band transition is being provided to the Services. The program office worked with Department of Navy Chief Information Officer (DoN CIO) and Office of the Chief of Naval Operations (OPNAV) for Information Dominance (N2/N6) on the appropriate use of the Spectrum Relocation Funds (SRF) and guidelines for spending and accounting of SRF dollars. The program office then led a SRF Planning Meeting on August 19, 2015 to plan the path forward for S-band integration into MIDS JTRS TTNT, the cost distribution between SRF and DoD funds, and the underlying assumptions for building the cost estimate for the L&S-Bands MIDS JTRS TTNT development. Expansion to S-Band impacts MIDS JTRS TTNT baseline, requiring redesign of the MIDS JTRS TTNT Transceiver (XCVR), MIDS JTRS TTNT External Power Amplifier (TEPA) and High Power Amplifier (HPA).

A successful L-Band MIDS JTRS TTNT XCVR risk reduction demonstration and early waveform porting was completed, which saved approximately five months of design and integration on the MIDS JTRS TTNT development effort. L-Band development continues and the award for the L&S-Bands MIDS JTRS TTNT design and development is anticipated in late FY 2016.

MIDS completed a review of PM Joint Tactical Network (JTN) processes for management of Software Defined Radio (SDR) waveforms in preparation for the transition of Link 16 waveform responsibilities to PMA/Program Management Warfare (PMW)-101. On June 4, 2015, all responsibilities of Link 16 waveform were transferred to PMA/PMW-101. Subsequently, PMA/PMW-101 participated in a Link 16 Evolution Kickoff Summit in Washington, DC on July 14, 2015. The meeting was chaired by Under Secretary of Defense for Acquisition, Acquisition, Technology, and Logistics (USD(AT&L)) Command, Control, and Communications (C3), Cyber and Business Systems (C3CB) and focused on ensuring DoD is evolving/modernizing Link 16 to increase future capabilities, and is fostering communication across DoD stakeholders.

MIDS-LVT Lot 16 delivery orders were awarded to DLS and ViaSat on August 31, 2015, 113 terminals and 8 receivers/transmitters units for \$21M. MIDS JTRS Lot 4 production was awarded to DLS and ViaSat on September 18, 2015, 209 terminals for \$70.8M.

There are no significant software-related issues with this program at this time.

History of Significant Developments Since Program Initiation:

April 1990: Joint Requirements Oversight Council Memorandum (JROCM 031-90) approved the Mission Need Statement (MNS) for MIDS-LVT.

December 1993: At MS II, USD(AT&L) authorized MIDS to proceed with MIDS-LVT EMD.

September 2001: USD(AT&L) directed the MIDS Program to update the Acquisition Strategy to include a JTRS Compliance Migration Strategy.

September 2003: At MS III, ASN(RDA) authorized Full Rate Production for MIDS-LVT.

July 2004: ASN(RDA) approved the Acquisition Strategy to develop MIDS JTRS via an Engineering Change Proposal.

February 2005: USD(AT&L) authorized the establishment of the Joint Program Executive Office (JPEO) Joint Tactical Radio System (JTRS) for authority over all JTRS products, including MIDS.

May 2008: JROCM 112-08 approved MIDS JTRS Capability Production Document.

December 2009: MIDS JTRS completed Contractor First Article Qualification Test and Government First Article Qualification Test (GFAQT). USD(AT&L) approved the Limited Production & Fielding of MIDS JTRS.

April 2011: MIDS JTRS completed Initial Operational Test & Evaluation including Verification of the Correction of Deficiencies(VCD), COMOPTEVFOR (Naval Command Operational Test and Evaluation Force) and Director of Operational Test & Evaluation Reports.

April 2012: USD(AT&L) approved the Full Production and Fielding of MIDS JTRS.

July 2012: USD(AT&L) directed the JPEO JTRS reorganization and realignment to transfer MIDS to Navy MDA alignment and designated MIDS as an ACAT IC program.

November 2012: ASN(RDA) approved MIDS JTRS IOC.

January 2013: ASN(RDA) designated MIDS as the Program Manager Air/Program Manager Warfare-101.

January 2013: ASN(RDA) authorized development of MIDS JTRS TTNT and MIDS JTRS CMN-4 capabilities to be managed as ECPs to the MIDS ACAT IC Program.

January 2013: PEO(Tactical Aircraft) assigned MIDS as the Naval Integrated Fire Control – Counter Air From the Air Advanced Tactical Data Link (ATDL) lead to coordinate with F/A-18, E-2D, EA-18G and other platform offices.

May 2013: Procurement, and Operating and Sustainment (O&S) breaches were realized due to increased procurement quantities of MIDS terminals by F/A-18. Program Deviation Report was submitted by the MIDS PM and approved by ASN (RD&A).

July 2013: MIDS JTRS CMN-4 Cooperative Development delivery orders were awarded to ViaSat and DLS.

November 2013: Due to the May Program Deviation Report, a revised Acquisition Program Baseline (APB) was approved by ASN(RD&A).

November 2013: MIDS-LVT Block Upgrade 2 (BU2) Award. MIDS-LVT BU2 development contracts were awarded to DLS, EuroMIDS and ViaSat. MIDS-LVT BU2 is a 39-month ECP to bring National Security Agency mandated Crypto Modernization and National Telecommunications and Information Agency and Federal Aviation Administration mandated Frequency Remapping capabilities to the MIDS-LVT Link-16 product line.

August 2014: MIDS JTRS TTNT L-Band Full Development Contract was awarded to DLS and ViaSat.

November 2014: MIDS JTRS TTNT waveform development was completed. The next step is early porting and demonstration of the waveform.

March 2015: Conducted the first MIDS JTRS CMN-4 flight on F/A-18 aircraft at China Lake.

May-June 2015: MIDS Modernization Increment 1 (MMI 1) demonstration testing was conducted, and development delivery orders were awarded to DLS and ViaSat.


June 2015: Responsibilities for the Link-16 waveform were transferred to MIDS program office from Joint Tactical Networking Center (JTNC).

August-September 2015: MIDS-LVT Lot 16 and MIDS JTRS Lot 4 production delivery orders were awarded to DLS and ViaSat.

Threshold Breaches

APB Breaches		Explanation of Breach
Schedule	<input type="checkbox"/>	The Procurement and O&S breaches occurred when the U.S. Air Force received the Resource Management Decision (RMD) funding for 1497 Concurrent Multi-Netting (CMN-4) and Tactical Targeting Network Technology (TTNT) MIDS Joint Tactical Radio System (JTRS) terminals in addition to the Navy 385 terminals. Additionally the services purchased 267 Low Volume Terminals (LVT). The PAUC and APUC overall continue below thresholds.
Performance	<input type="checkbox"/>	
Cost	<input type="checkbox"/>	
RDT&E	<input type="checkbox"/>	
Procurement	<input checked="" type="checkbox"/>	
MILCON	<input type="checkbox"/>	A Program Deviation Report (PDR) was signed by the MIDS PM on February 16, 2016. The PDR was submitted to PEO(T) for review and forwarding to the Assistant Secretary of the Navy for Research, Development, and Acquisition (ASN RD&A). A revised APB is in process.
Acq O&M	<input type="checkbox"/>	
O&S Cost	<input checked="" type="checkbox"/>	
Unit Cost	<input type="checkbox"/>	
PAUC	<input type="checkbox"/>	
APUC	<input type="checkbox"/>	
Nunn-McCurdy Breaches		
Current UCR Baseline		
PAUC	None	
APUC	None	
Original UCR Baseline		
PAUC	None	
APUC	None	

Schedule

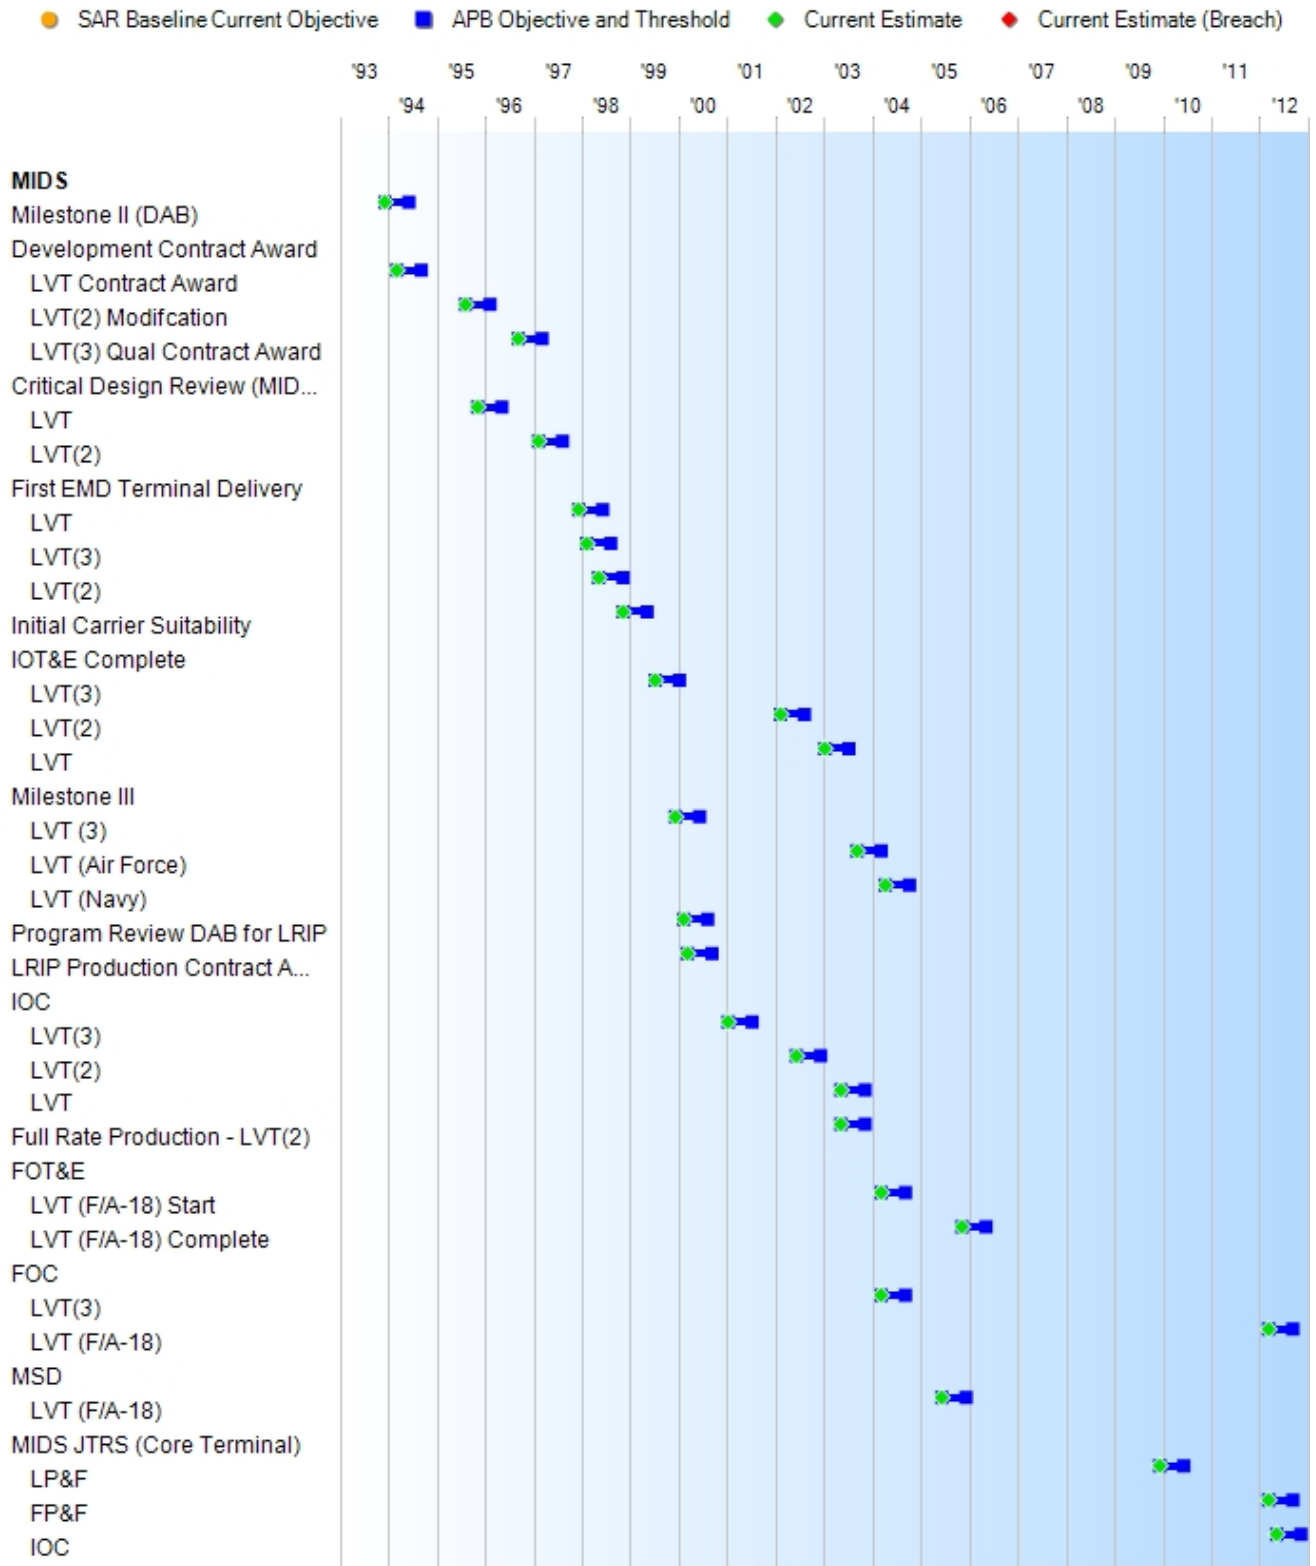

Schedule Events				
Events	SAR Baseline Production Estimate	Current APB Production Objective/Threshold		Current Estimate
Milestone II (DAB)	Dec 1993	Dec 1993	Jun 1994	Dec 1993
Development Contract Award				
LVT Contract Award	Mar 1994	Mar 1994	Sep 1994	Mar 1994
LVT(2) Modification	Aug 1995	Aug 1995	Feb 1996	Aug 1995
LVT(3) Qual Contract Award	Sep 1996	Sep 1996	Mar 1997	Sep 1996
Critical Design Review (MIDS Terminal)	N/A			
LVT	Nov 1995	Nov 1995	May 1996	Nov 1995
LVT(2)	Feb 1997	Feb 1997	Aug 1997	Feb 1997
First EMD Terminal Delivery				
LVT	Dec 1997	Dec 1997	Jun 1998	Dec 1997
LVT(3)	Feb 1998	Feb 1998	Aug 1998	Feb 1998
LVT(2)	May 1998	May 1998	Nov 1998	May 1998
Initial Carrier Suitability	Nov 1998	Nov 1998	May 1999	Nov 1998
IOT&E Complete				
LVT(3)	Jul 1999	Jul 1999	Jan 2000	Jul 1999
LVT(2)	Feb 2002	Feb 2002	Aug 2002	Feb 2002
LVT	Jan 2003	Jan 2003	Jul 2003	Jan 2003
Milestone III				
LVT (3)	Dec 1999	Dec 1999	Jun 2000	Dec 1999
LVT (Air Force)	Sep 2003	Sep 2003	Mar 2004	Sep 2003
LVT (Navy)	Apr 2004	Apr 2004	Oct 2004	Apr 2004
Program Review DAB for LRIP	Feb 2000	Feb 2000	Aug 2000	Feb 2000
LRIP Production Contract Award	Mar 2000	Mar 2000	Sep 2000	Mar 2000
IOC				
LVT(3)	Jan 2001	Jan 2001	Jul 2001	Jan 2001
LVT(2)	Jun 2002	Jun 2002	Dec 2002	Jun 2002
LVT	May 2003	May 2003	Nov 2003	May 2003
Full Rate Production - LVT(2)	May 2003	May 2003	Nov 2003	May 2003
FOT&E				
LVT (F/A-18) Start	Mar 2004	Mar 2004	Sep 2004	Mar 2004
LVT (F/A-18) Complete	Nov 2005	Nov 2005	May 2006	Nov 2005
FOC				
LVT(3)	Mar 2004	Mar 2004	Sep 2004	Mar 2004
LVT (F/A-18)	Mar 2012	Mar 2012	Sep 2012	Mar 2012

MSD				
LVT (F/A-18)	Jun 2005	Jun 2005	Dec 2005	Jun 2005
MIDS JTRS (Core Terminal)				
LP&F	N/A	Dec 2009	Jun 2010	Dec 2009
FP&F	N/A	Mar 2012	Sep 2012	Mar 2012
IOC	N/A	May 2012	Nov 2012	May 2012

Change Explanations

None

Notes

An OSD decision was made in December 2009 that MIDS Joint Tactical Radio System (MIDS JTRS) (Core Terminal) did not require a Milestone (MS) C decision since the MIDS Program had a MS C decision in September 2003.

Acronyms and Abbreviations

FOT&E - Follow-On Test and Evaluation
 FP&F - Full Production and Fielding
 IOT&E - Initial Operational Test and Evaluation
 JTRS - Joint Tactical Radio System
 LP&F - Limited Production and Fielding
 LVT - Low Volume Terminal
 MSD - Material Support Date
 Qual - Qualification

Performance

Performance Characteristics				
SAR Baseline Production Estimate	Current APB Production Objective/Threshold		Demonstrated Performance	Current Estimate
Interoperability				
All top level IERs in SMORD	All top level IERs in SMORD	All critical top level IERs in SMORD	100% Demonstrated	All top level IERs in SMORD
Waveform Compatibility				
STANAG 4175 & JTIDS SSS	STANAG 4175 & JTIDS SSS	STANAG 4175 & JTIDS SSS	JITC Certified	STANAG 4175 & JTIDS SSS
Message Standard				
STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016B	STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016B	STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016B	JITC Certified	STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016B
Maximum Power Transmission (w)				
LVT				
Multiple selectable levels	Multiple selectable levels	>=200 with IF for 1000	200 with IF	Multiple selectable levels
LVT(2)				
Multiple selectable levels	Multiple selectable levels	>=200 or 25 selectable	200/25	Multiple selectable levels
LVT(3)				
Multiple selectable levels	Multiple selectable levels	>=50	50	Multiple selectable levels
IER (Kbps)				
1000	>=1000	28.8 -115.2	1100 kbps	>=1000
Paired Time Slot Relay Capability				
Integral and automated	Integral and automated	Integral and automated	Integral and automated	Integral and automated
Repromulgation Relay (nm) MIDS-LVT(2)				
4 hop	4 hops	3 hops	4 hops	4 hops
Paired Time Slot Relay Range (nm) (USN Only)				

1200	>=1200	>=500	520	>=1200
Communication Range				
LVT (USN: C2 to C2)				
300	>=300	>=300	350	>=300
LVT (USN: Non-C2 to C2)				
240	>=240	>=220	240	>=240
LVT (USN: Non-C2 to Non-C2)				
200	>=200	>=180	220	>=200
LVT (USN: Surface Platforms)				
LOS up to 300	LOS >=300	LOS >=300	300	LOS >=300
LVT (F-16: Non-C2 to C2)				
300	>=300	>=200	200	>=300
LVT (F-16: Non-C2 to Non-C2)				
150	>=150	>=100	150	>=150
LVT(2)				
Up to 300 with LOS at 200 w	Up to 300 with LOS at 200 w	Up to 300 with LOS at 200 w	300	Up to 300 with LOS at 200 w
LVT(3) (Non-C2 to C2)				
300	>=300	>=200	300	>=300
LVT(3) (Non-C2 to Non-C2)				
150	>=150	>=100	170	>=150
Voice Channels: LVT (USN)				
Capable of 2	Capable of 2	1	2	Capable of 2
Coded Message Error Probability (%)				
LVT				
1	<=1	<=2	Passed	<=1
LVT(3)				
< 1 detected	<= 1 detected	<=2	Passed	<= 1 detected
LVT(2)				
1	<=1	<=2	Passed	<=1
Jam Resistance				
LVT (USN) (db)				
MJCS-194 - 89	MJCS-194-89	MJCS-194-89	Compliant	MJCS-194-89
LVT (F-16) (%)				
< 1 detected error	<=1 detected error	<= 1 detected error	Passed	<=1 detected error

LVT(2) (%)				
< 1 detected error	<= 1 detected error	<= 5	Passed	<= 1 detected error
LVT(3) (%)				
< 1 detected error	<= 1 detected error	<= 1 detected error	Passed	<= 1 detected error
Ao				
LVT				
.90	>=.90	>=.90	.91	>=.90
LVT(2) (Terminal)				
.94	>=.94	>=.90	.94	>=.94
LVT(3)				
.97	>=.97	>=.95	.965	>=.97
MTBF (hr)(lab)				
USN				
1000	>=1000	>=1000	1850	>=1000
USA				
1800	>=1800	>=1000	1850	>=1800
USAF				
1500	>=1500	>=1000	1850	>=1500
MFHBOMF/MTBOMF (hr)				
System				
25	>=25	>=25	32	>=25
LVT (Aircraft) (Terminal)				
300	>=300	>=220	240	>=300
LVT (Ships) (Terminal)				
350	>=350	>=257	275	>=350
LVT(2) (Terminal)				
393	>=393	>=393	425	>=393
MTTR (O-level) (min)				
LVT(2) (Terminal)				
30	<=30	<=30	25	<=30
MCMTOMF				
LVT (USN Aircraft)				
60	<=60	<=90	75	<=60
LVT (USN Ships)				
60	<=60	<=90	80	<=60
LVT (USAF)				

MRT < 20	MRT < 20	MRT < 30	25	MRT < 20
LVT(3)				
MRT < 20	MRT < 20	MRT < 30	28	MRT < 20
Volume (Cubic Feet)				
LVT				
< .6	<= .6	<= .6	.58	<= .6
LVT(2)				
< 1.4	<=1.4	<=1.4	1.32	<=1.4
LVT(3)				
< .6	<= .6	<= .6	.56	<= .6
Weight (lbs)				
LVT				
< 65	<=65	<=65	63.8	<=65
LVT(2)				
< 88	<=88	<=88	87.9	<=88
LVT(3)				
< 65	<=65	<=65	63.8	<=65
MIDS-LVT Enhancement ECPs				
Message Standards				
N/A	STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016C	STANAG 5516 (& 5516 for Data Fwds) & MIL-STD-6016B	To Be Determined (TBD) until Block Upgrade 2 (BU2) Enhanced Throughput (ET) is implemented	STANAG 5516 (& 5616 for Data Fwds) & MIL-STD-6016C
Communications Range				
N/A	see note 12c through 17c	see note 12c through 17c	TBD until MIDS-LVT BU2 ET is implemented	TBD until MIDS-LVT BU2 is implemented
Information Exchange Rate (Kbps)				
LET 0				
N/A	>=358	>=107	TBD until MIDS-LVT BU2 ET is implemented	>=358
LET 1				
N/A	>=546	>=358	TBD until MIDS-LVT BU2 ET is implemented	>=546
LET 2				
N/A	>=833	>=546	TBD until MIDS-LVT BU2 ET is	>=833

			implemented	
LET 3				
N/A	>=968	>=833	TBD until MIDS-LVT BU2 ET is implemented	>=968
LET 4				
N/A	>=1100	>=968	TBD until MIDS-LVT BU2 ET is implemented	>=1100
Coded Message Error Probability (%)				
LET 0				
N/A	<=1%	<=2%	TBD until MIDS-LVT BU2 ET is implemented	<=1%
LET 1				
N/A	<=1%	<=2%	TBD until MIDS-LVT BU2 ET is implemented	<=1%
LET 2				
N/A	<=1%	<=2%	TBD until MIDS-LVT BU2 ET is implemented	<=1%
LET 3				
N/A	<=1%	<=2%	TBD until MIDS-LVT BU2 ET is implemented	<=1%
LET 4				
N/A	<=1%	<=2%	TBD until MIDS-LVT BU2 ET is implemented	<=1%
Jam Resistance				
N/A	MJCS-194-89	MJCS-194-89	TBD until MIDS-LVT BU2 ET is implemented	MJCS-194-89
MIDS JTRS Performance Parameters				
Link-16 Waveform compatibility				
N/A	STANAG 4175 and MIDS LVT SSS	STANAG 4175 and MIDS LVT SSS	Passed JITC waveform conformance test.	Passed JITC waveform conformance test.
Link-16 Message Standard				
N/A	MIL-STD-6016C and STANAG 5516	MIL-STD-6016C and STANAG 5516	Passed JITC waveform conformance test.	Passed JITC waveform conformance

				test.
Link-16 IER				
Normal Operations with JTRS				
N/A	>=1100 Kbps	>=28-115.2 Kbps	128	128
LET 0				
N/A	>=358	>=107	107	107
LET 1				
N/A	>=546	>=358	358	358
LET 2				
N/A	>=833	>=546	546	546
LET 3				
N/A	>=968	>=833	837	837
LET 4				
N/A	>=1100	>=968	968	968
Interoperability: All top level IERs will be satisfied to the standards specified in the threshold (T) and objective (O) values.				
N/A	All top-level Information exchange Requirements (IERs) are met.	All top-level Information Exchange Requirements (IERs) are met.	All top-level IERs transferred.	All top-level IERs transferred.
Link-16 Coded Message Error Probability (CMEP)				
LET 0				
N/A	<=1%	<=2%	<=2%	<=1%
LET 1				
N/A	<=1%	<=2%	<=2%	<=1%
LET 2				
N/A	<=1%	<=2%	<=2%	<=1%
LET 3				
N/A	<=1%	<=2%	<=2%	<=1%
LET 4				
N/A	<=1%	<=2%	<=2%	<=1%
Weight/Volume				
N/A	<=65 lbs, <=.6 cu.ft.	<=65 lbs, <=.6 cu.ft.	Measured 54.7 lbs; measured .573 cu. ft.	<=65 lbs, <=.6 cu.ft.
Link-16 Jam Resistance				
JTRS (USN) (db)				
N/A	MJCS-194-89	MJCS-194-89	Exceeds threshold by 1-3 db in 95% of all cases.	Exceeds threshold by 1-3 db in 95% of all cases.

All Others				
N/A	<=1% Detected message error rate	<=1% Detected message error rate	.98%	.98%
Link-16 J-Voice Channels				
N/A	2	2	2	2
Link-16 Communications Range Data				
N/A	≥300 nm (C2-C2 w/HPA); ≥240 nm (C2-non-C2); ≥200 nm (non-C2-non-C2)	≥300 nm (C2-C2 w/HPA); ≥220 nm (C2-non-C2); ≥180 nm (non-C2-non-C2)	≥250 nm	≥250 nm.
Link-16 Communications Range J-Voice				
N/A	≥220nm (C2-C2 w/HPA); ≥140nm (C2-non-C2); ≥90nm (non-C2-nonC2/non C2-C2)	≥220nm (C2-C2 w/HPA); ≥140nm (C2-non-C2); ≥90nm (non-C2-nonC2/non C2-C2)	≥220nm (C2-C2 w/HPA) - Not Tested; ≥140nm (C2-non-C2 - Not tested; ≥90nm (non-C2-nonC2/non C2-C2) - 150.	≥220nm (C2-C2 w/HPA) - Terminal not installed in C2 platform yet; ≥140nm (C2-non-C2 - Terminal not installed in C2 platform yet; ≥90nm (non-C2-nonC2/non C2-C2) - 150.
Link-16 Relay				
N/A	≥1200nm	≥500nm	Not tested yet.	≥500 nm
Multi-Channels/Networks				
N/A	4 Channels simultaneously with TACAN/multi-net (single network) Link-16 fixed operation on Channel 1	4 Channels simultaneously with TACAN/multi-net (single network) Link-16 fixed operation on Channel 1	4 Channels passed.	4 Channels passed.
Scan Frequencies				
N/A	Scan a minimum of 10 frequencies or presets	Scan a minimum of 10 frequencies or presets	FOT&E: No MIDS JTRS waveforms require presets.	FOT&E: No MIDS JTRS waveforms require presets.
Terminal Start-up/Restart (Link-16 only)				
N/A	<=2.0 min	<=3.5 minutes	3.2 min	3.2 min
IBIT Performance (Link-16 only)				
N/A	<=30seconds	<=70 seconds	29 seconds	29 seconds
Link-16 Net Entry/Synchronization				
N/A	<=30 seconds	Not to exceed 4 min from time that coarse sync is initiated	30 sec - 2.5 min	30 sec - 2.5 min
Crypto-Rekeying				
N/A	Over the Air Rekeying	At O-level	Not implemented in	Not implemented

	(OTAR) through electronic media, or common reprogramming hardware / software		Core Terminal.	in Core Terminal.
Link-16 Transmission of Unit Position and Status Reports				
N/A	<=100 ft accuracy	<=300 ft accuracy	78 ft	78 ft
TACAN Performance Start-up/Restart				
N/A	<=14 seconds	<=30 seconds	15 seconds	15 seconds
MFHBOMF (System/Single Channel)				
N/A	>=36 hrs (Other Platforms)	>=25 hrs (F/A-18E/F, EA-18G, TACAIR)	36.5 hrs.	36.5 hrs
MTBF Lab (Ch. 1(Link-16))				
N/A	>=1800 hrs	>= 1200 hrs	1285 hrs	1285 hrs
MTBF Lab (Ch. 2, 3 & 4)				
N/A	>=1800 hrs	>=1550 hrs	1550 hrs	1550 hrs
MFHBOMF (Terminal/Single Channel)				
N/A	>=300 hrs	>=220 hrs	724 (includes lab data)	220 hrs
MCMTOMF (Single Channel)				
N/A	<= 60 min	<=120 min; <= 90 min (F/A-18 E/F, EA-18G, NAVAIR)	60 min	60 min (Single channel)
MRT				
N/A	<= 20 min	<= 45 min	20 min	45 min
BIT PCD				
N/A	PCD>= 98%	PCD>= 95%	97%	97%
BIT MFHBFA				
N/A	MFHBFA: >= 451 hrs	MFHBFA: >= 113 hrs	80 hrs	120 hrs
Start-Up (Terminal/Single Channel)				
N/A	<=2min (OE, crypto and waveform); <=2min (fine sync)	<=3.5min (OE, Crypto and waveform); <=4min (fine sync)	3.2 min	3.2 min
Start-Up (Waveform/Link-16 only)				
N/A	<=2min (OE, crypto, and waveform); <=2min (fine sync)	<=3.5min (OE, crypto, and waveform); <=4min (fine sync)	.5 - 2.5 min	.5 - 2.5 min
Restart < 50 milliseconds (Core configuration only)				
N/A	Operates through	Operates through	Operates through	Operates through
Restart <10 seconds (Terminal)				
N/A	<=2min	<=3.5min	2.5 min	2.5 min
Restart <10 seconds (Link-16 waveform)				

N/A	<=10sec	<=10sec	9 sec	9 sec
Restart >=10 seconds and <2min (Terminal)				
N/A	<=2min	<=3.5min	3.2 min	3.2 min
Restart >=10 seconds and <2min (Link-16)				
N/A	<=2min	<=4min	3.2 min	3.2 min
Restart >= 2 min (Terminal)				
N/A	<=2min	<=3.5min	3.2 min	3.2 min
Restart >=2 min (Link-16 Waveform)				
N/A	<=2min	<=4min	3.2 min	3.2 min
TACAN Start-up/Restart				
N/A	<=14sec	<=30sec	15 sec	15 sec
IBIT Performance				
N/A	<=30sec	<=70sec	30 sec	30 sec
Terminal Operating Frequency Range				
N/A	Operate 2-2000 MHz	Operate 2-2000 MHz	Operation within 2-2000 MHz	Operate 2-2000 MHz
MIDS JTRS Capability				
N/A	F3I for MIDS-LVT (1) and shall meet the performance measures in MIDS JTRS Core Terminal in Table 6 of the CPD in addition to TACAN and J-Voice.	F3I for MIDS-LVT (1) and shall meet the performance measures in MIDS JTRS Core Terminal in Table 6 of the CPD in addition to TACAN and J-Voice.	11 of 11 Performance measures have been achieved in a Developmental Test period.	11 of 11 Performance measures have been achieved in a Developmental Test period.
Functionality				
N/A	MIDS JTRS Core Terminal will meet connectivity requirements of ALL Airborne (MIDS JTRS) Domain Waveforms.	The MIDS JTRS Core Terminal shall be capable of supporting secure and non-secure voice, video, and data communications by porting narrowband and wideband JTRS developed waveforms in compliance with the Software Communications Architecture. Where a MIDS JTRS Core Terminal replaces the WF/radio function(s) of one or more legacy radios and continued interoperability with legacy radios is required, software WFs will be ported and JTRS radio shall perform the same WF/radio function(s) and mission(s) supported by the legacy radios. JTRS Core Terminal will meet connectivity requirements of ported Waveforms.	15 of 15 Performance measures have been achieved.	15 of 15 Performance measures have been achieved.

Number of Channels				
N/A	Threshold same as Objective (One TACAN/Link-16 plus three additional channels for JTRS Waveforms).	One TACAN/Link-16 plus three additional channels for JTRS Waveforms. Navy Initial Implementation - TACAN/Link-16 plus 3 additional channels ((2MHz - 2 GHz transceivers) as capability for future JTRS WFs) for F/A-18E/F. USAF Initial Implementation - Link-16 for B-1.	1 of 1 Performance measures have been achieved.	1 of 1 Performance measures have been achieved.
Net Ready				
N/A	The system must fully support execution of joint critical operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for transition to Net-Centric military operations to include 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration (Table 31), 3) NCOW RM Enterprise Services 4) IA requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an IATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture reviews.	The MIDS JTRS Core Terminal will support Net-Centric military operations via a gateway. The system must be able to enter and be managed in the network, and exchange data in a secure manner to enhance mission effectiveness. The systems must have the ability to provide survivable, interoperable, secure and operationally effective information exchanges to enable a Net-centric military capability. The system must fully support execution of all operational activities identified in the applicable joint and system integrated architectures and the system must satisfy the technical requirements for Net-Centric military operations to include 1) DISR mandated GIG IT standards and profiles identified in the TV-1, 2) DISR mandated GIG KIPs identified in the KIP declaration (Table 31), 3) NCOW RM Enterprise Services 4) IA requirements including availability, integrity, authentication, confidentiality, and non-repudiation, and issuance of an ATO by the DAA, and 5) Operationally effective information exchanges; and mission critical performance and information assurance attributes, data correctness, data availability, and consistent data processing specified in the applicable joint and system integrated architecture reviews.	5 of 5 Performance measures have been achieved. System certified by NSA in March 2010	5 of 5 Performance measures have been achieved. System certified by NSA in March 2010.

Operational Availability (Ao)				
N/A	Each MIDS JTRS Core Terminal shall demonstrate an Ao of >0.99 for all channels.	Each MIDS JTRS Core Terminal shall demonstrate an Ao of >0.90 for Link-16 / TACAN Channel and >0.96 for the remaining channels.	96.8%.	96.8%
Software Configurable				
N/A	Each MIDS JTRS Core Terminal shall provide any designated operator with the ability to load and reconfigure its modes/capabilities via software while in the operational environment	Each MIDS JTRS Core Terminal shall provide any designated operator with the ability to load and reconfigure its modes/capabilities via software while in the operational environment	1 of 1 Performance measures have been achieved.	1 of 1 Performance measures have been achieved.
Growth				
N/A	MIDS JTRS Core Terminal shall provide an internal growth capability through an open systems architecture approach, and shall be modular, scaleable and flexible as designed to suit specific operational requirements.	MIDS JTRS Core Terminal shall provide an internal growth capability through an open systems architecture approach, and shall be modular, scaleable and flexible as designed to suit specific operational requirements.	2 of 2 Performance measures achieved.	2 of 2 Performance measures achieved.
Navigation – Link-16 Position (PPLI)				
N/A	≤100 feet	≤300 feet	Operation at ≤100 feet	≤100 feet
Tactical Air Navigation (TACAN)				
N/A	Capabilities equivalent to LVT	Capabilities equivalent to LVT	Capabilities equivalent to LVT	Capabilities equivalent to LVT
Spectrum Certification				
N/A	Meets DD-1494 Stage 4	Meets DD-1494 Stage 4	DD-1494 Stage 4 issued.	Meets DD-1494 Stage 4
Memory/Processor Reserve				
N/A	Provide growth memory and processor reserve to allow for an increased capability or functionality of each set and with each generation of radios	Provide growth memory and processor reserve to allow for an increased capability or functionality of each set and with each generation of radios	Met with no issues.	Provide growth memory and processor reserve to allow for an increased capability or functionality of each set and with each generation of radios
Operational Communications				
Passive Synchronization				

N/A	Fine Sync achieved passively	Fine Sync achieved passively	Achieved Fine Sync passively	Fine Sync achieved passively
Automatic Message Acknowledgement				
N/A	IAW Mil-STD 6016C	IAW Mil-STD 6016C	Automatic Message Acknowledgement IAW Mil-STD 6016C	IAW Mil-STD 6016C
Crypto Control (CTP-11)				
N/A	Proper O-level control of NSA approved crypto device	Proper O-level control of NSA approved crypto device	Proper O-level control of NSA approved crypto device	Proper O-level control of NSA approved crypto device
Multi-Net (CTP-10)/8d				
N/A	2 simultaneous nets	2 simultaneous nets	Performance of two simultaneous nets	2 simultaneous nets
GIG Requirements				
N/A	DISR mandated GIG requirements specified in TV-1 of ISP	DISR mandated GIG requirements specified in TV-1 of ISP	Met DISR mandated GIG requirements specified in TV-1 of ISP	DISR mandated GIG requirements specified in TV-1 of ISP
Key Information Profile (KIP)				
N/A	DISA mandated GIG KIPs are identified in ISP in the KIP Declaration Table	DISA mandated GIG KIPs are identified in ISP in the KIP Declaration Table	The DISA mandated GIG KIPs are identified in the ISP in the KIP Declaration Table	DISA mandated GIG KIPs are identified in ISP in the KIP Declaration Table
Design per NCOW RM				
N/A	NCOW RM Enterprise Services are met	NCOW RM Enterprise Services are met	The NCOW RM Enterprise Services are met	NCOW RM Enterprise Services are met
Information Exchange Requirements met				
N/A	Operationally Effective exchanges of all messages IAW ISP	Operationally Effective exchanges of all messages IAW ISP	Showed Operationally Effective exchange of all messages IAW ISP	Operationally Effective exchanges of all messages IAW ISP
Enable CMN/CCR Reception				
N/A	Receive on 4 net numbers (CMN); 4 receptions within a timeslot (CCR)	Receive on 4 net numbers (CMN); 4 receptions within a timeslot (CCR)	TBD	Receive 4 net numbers (CMN); 4 receptions within a timeslot (CCR)

Requirements Reference

MIDS Operational Requirements Document (ORD) (MIDS-LVT) dated July 25, 2004 and MIDS JTRS Capability Production Document (CPD) dated July 16, 2013

Change Explanations

None

Notes

1. For LET 0 there is a 5 db loss in jam resistance and 44% loss in range over PAC4 Single Pulse. The 1% error rate will be calculated based on the decrease in jamming resistance.
2. For LET 1 there is a 7 db loss in jam resistance and 56% loss in range over PAC4 Single Pulse. The 1% error rate will be calculated based on the decrease in jamming resistance.
3. For LET 2 there is a 9 db loss in jam resistance and 65% loss in range over PAC4 Single Pulse. The 1% error rate will be calculated based on the decrease in jamming resistance.
4. For LET 3 there is a 10 db loss in jam resistance and 67% loss in range over PAC4 Single Pulse. The 1% error rate will be calculated based on the decrease in jamming resistance.
5. For LET 4 there is an 11 db loss in jam resistance and 72% loss in range over PAC4 Single Pulse. The 1% error rate will be calculated based on the decrease in jamming resistance.
6. For Frequency Remap, there will be a db loss for the number of frequencies remapped based on the formula $10 \log(51/51-NR)$ where NR = the number of frequencies remapped. There is a corresponding decrease in range of approximately 1% for each frequency that is remapped.

Acronyms and Abbreviations

Ao - Operational Availability
ATO - Authority to Operate
BIT - Built in Test
BU2 - Block Upgrade 2
C2 - Command and Control
CFAQT - Contractor First Article Qualification Testing
CMEP - Coded Message Error Probability
CMN/CCR - Concurrent Multi-Netting/Concurrent Contention Receive
cu. ft. - cubic feet
DAA - Designated Approving Authority
db - decibel(s)
DISR - Defense Information Standards Registry
ECP - Engineering Change Proposal
ET - Enhanced Throughput
F3I - Form, Fit, Function and interface
FDL - Fighter Data Link
FOT&E - Follow-on Test and Evaluation
GFAQT - Government First Article Qualification Testing
GIG IT - Global Information Grid Information Technology
HPA - High Power Amplifier
hr - hour(s)
IATO - Interim Authority to Operate
IBIT - Initialization Built in Test
IER - Information Exchange Requirements
IF - Interface
JITC - Joint Interoperability Test Command
JTIDS - Joint Tactical Information Distribution System
kbps - kilobits per second
KIPs - Key Interface Profiles
lbs - Pounds
LET - Link 16 Enhanced Throughput
LOS - Line of sight
LVT - Low Volume Terminal
MCMTOMF - Mean Corrective Maintenance Time for Operational Mission Failures
MFHBFA - Mean Flight Hours Between False Alarms
MFHBOMF - Mean Flight Hours Between Operational Mission Failures
MHz - Megahertz
MIDS - Multifunctional Information Distribution System
Mil-Std - Military Standard
min - minute(s)
MJCS - Memorandum Joint Chiefs of Staff
MRT - Mean Repair Time
MTBF - Mean Time Between Failure
MTBOMF - Mean Time Between Operational Mission Failures
MTTR - Mean Time to Repair
NCOW RM - Net-Centric Operations and Warfare Reference Model
nm, nmi - Nautical mile
NSA - National Security Agency
OE - Operational Environment
O-Level - Organization Level
OTAR - Over the Air Re-keying
PAC4 - Packed-4

PCD - Percent Correct Detect

sec - second(s)

SINGARS - Single Channel Ground and Airborne Radio System

SMORD - Single MIDS ORD

SSS - System Segment Specification

STANAG - Standardization Agreement

TACAN - Tactical Air Navigation

TV - Technical View

w - watt(s)

Track to Budget

General Notes

The current RDT&E increased to fully fund MIDS Joint Tactical Radio System (JTRS) Tactical targeting Network technology (TTNT) development.

The current production terminal procurement estimate increased by a total of 2,149 terminals due to the large procurement order from the U.S. Air Force (Platforms: F-15, F-16, F-22).

RDT&E

Appn	BA	PE		
Navy	1319	05	0205604N	
	Project		Name	
	2126		Tactical Data Links	(Shared) (Sunk)
	Notes:	ATDLS Integration		
Navy	1319	07	0205604N	
	Project		Name	
	2126		Tactical Data Links	(Shared)
	Notes:	ATDLS Integration		
	3020		Tactical Data Links	(Shared)
	Notes:	MIDS/JTRS		
Navy	1319	05	0604234N	
	Project		Name	
	3051		Advanced Hawkeye	(Shared)
Navy	1319	05	0604270N	
	Project		Name	
	E0556		Navy EA-6B Integration/EA-6B	(Shared) (Sunk)
	E2781		Navy EA-6B Integration/EA-6B	(Shared) (Sunk)
Navy	1319	05	0604280N	
	Project		Name	
	3020		Joint Tactical Radio System (JTRS)	(Shared) (Sunk)
	Notes:	MIDS/JTRS		
	3073		Joint Tactical Radio System (JTRS)	(Shared) (Sunk)
	Notes:	AMF/JTRS		
Army	2040	05	0603713A	
	Project		Name	
	D370			(Shared) (Sunk)
	Notes:	Army MIDS/Army MIDS		
Army	2040	05	0604280A	
	Project		Name	
	162		Joint Tactical Radio System	(Shared) (Sunk)

(JTRS)

Notes: Network Enterprise Domain (NED)

Air Force	3600	07	0101126F	
	Project		Name	
	675344		B-1B Squadrons	(Shared)
Air Force	3600	07	0101127F	
	Project		Name	
	675345		B-2 Squadrons	(Shared)
Air Force	3600	05	0207130F	
	Project		Name	
	F15		Air Force MIDS/F-15C/D	(Shared) (Sunk)
Air Force	3600	07	0207133F	
	Project		Name	
	672671		F-16 Squadrons	(Shared)
Air Force	3600	05	0207133F	
	Project		Name	
	672671		Air Force MIDS/F-16	(Shared) (Sunk)
Air Force	3600	05	0207134F	
	Project		Name	
	674703		Air Force MIDS/F-15E	(Shared) (Sunk)
Air Force	3600	07	0207134F	
	Project		Name	
	676020		F-15 Squadrons	(Shared)
Air Force	3600	07	0207138F	
	Project		Name	
	674788		F-22 Squadrons	(Shared)
Air Force	3600	07	0207417F	
	Project		Name	
	67411L		Airborne Warning and Control System (AWACS)	(Shared)
Air Force	3600	07	0207448F	
	Project		Name	
	675045		C2ISR Tactical Data Link	(Shared)
Air Force	3600	07	0208006F	
	Project		Name	
	675380		Mission Planning Systems	(Shared)
Air Force	3600	07	0305207F	
	Project		Name	
	674754		Manned Reconnaissance Systems	(Shared)
Air Force	3600	05	0604240F	
	Project		Name	
	11B002		Air Force MIDS	(Shared) (Sunk)

Air Force	3600	05	0604280F
	Project		Name
	655068		Joint Tactical Radio System (JTRS) (Shared) (Sunk)

Air Force	3600	05	0604281F
	Project		Name
	655050		Tactical Data Networks Enterprise (Shared)

Defense-Wide	0400	05	0603883C
	Project		Name
	0010		DOD (Shared) (Sunk)

Defense-Wide	0400	05	0604771D
	Project		Name
	P771		OSD, DA/JTRS (Shared) (Sunk)
	P773		OSD, DA/Multifunctional Information Distribution System (Shared) (Sunk)

Procurement

	Appn	BA	PE
Navy	1506	01	0204136N
	Line Item		Name
	0145		F-18 Series (Shared) (Sunk)

Navy	1506	05	0204154N
	Line Item		Name
	0511		EA-6 Series (Shared)

Navy	1506	05	0204136N
	Line Item		Name
	0525		F-18 Series (Shared)

Navy	1506	05	0204152N
	Line Item		Name
	0544		EW Development (Shared) (Sunk)
	Notes:		EA-6 Series Sunk FY16

Navy	1611	02	0204112N
	Line Item		Name
	2001		Carrier Replacement Program (Shared)
	2086		Multi-Purpose CVNs (Shared) (Sunk)

Navy	1611	02	0204222N
	Line Item		Name
	2122		DDG (Shared)

Navy	1611	02	0204230N
	Line Item		Name
	2127		Littoral Combat Ship (Shared)

Navy	1611	03	0204411N
	Line Item		Name
	3035		Amphibious Assault Ships (Shared) (Sunk)
	3036		LPD-17 (Shared)
Navy	1611	05	0204411N
	Line Item		Name
	5110		Outfitting (Shared)
Navy	1810	02	0205604N
	Line Item		Name
	2614		Advanced Tactical Data Link System (Shared)
Army	2035	02	0214400A
	Line Item		Name
	B22603		Radio Terminal Set, MIDS-LVT (2) (Shared)
Air Force	3010	05	0604281F
	Line Item		Name
	655262		Tactical Data Networks Enterprise (Shared)
Air Force	3010	05	0207446F
	Line Item		Name
	B00200		ABL (Shared)
Air Force	3010	07	0207132F
	Line Item		Name
	F01500		F-15 (Shared)
Air Force	3010	05	0207130F
	Line Item		Name
	F01500		F-15 (Shared) (Sunk)
Air Force	3010	05	0207133F
	Line Item		Name
	F01600		F-16 (Shared)
Air Force	3010	07	0207133F
	Line Item		Name
	F0160P		F-16 (Shared) (Sunk)
Air Force	3010	05	0207423F
	Line Item		Name
	MN9860		Joint Tactical Radio System (Shared)
Air Force	3010	05	0207133F
	Line Item		Name
	OTHACF		Other Aircraft (Shared)
	Notes:		Battlefield ABN Comm Node (BACN)
Air Force	3080	03	0207448F
	Line Item		Name

831010 Comsec Equipment (Shared)
 834010 General Information (Shared)
 Technology

Air Force 3080 03 0401840F

Line Item	Name
834070	AMC Command and Control System

 (Shared)

Air Force 3080 03 0201131F

Line Item	Name
835140	Air Combat Command Communications

 (Shared)
Notes: AFCENT

Air Force 3080 02 0207133F

Line Item	Name
F01600	F-16

 (Shared) (Sunk)

Defense-Wide 0300 02

Line Item	Name
10	DOD

 (Shared) (Sunk)

Defense-Wide 0300 02 0208865C

Line Item	Name
2257	DA, Patriot

 (Shared) (Sunk)

Defense-Wide 0300 02 0208861C

Line Item	Name
2260	DA, THAAD

 (Shared) (Sunk)

Defense-Wide 0300 02

Line Item	Name
30	GAPO

 (Shared) (Sunk)

Cost and Funding

Cost Summary

Total Acquisition Cost							
Appropriation	BY 2003 \$M			BY 2003 \$M	TY \$M		
	SAR Baseline Production Estimate	Current APB Production Objective/Threshold		Current Estimate	SAR Baseline Production Estimate	Current APB Production Objective	Current Estimate
RDT&E	869.4	1637.5	1801.3	1738.8	825.8	1750.6	1877.0
Procurement	955.4	1393.5	1532.9	2133.5 ¹	993.1	1585.6	2615.7
Flyaway	--	--	--	1946.3	--	--	2407.1
Recurring	--	--	--	1873.8	--	--	2335.7
Non Recurring	--	--	--	72.5	--	--	71.4
Support	--	--	--	187.2	--	--	208.6
Other Support	--	--	--	39.8	--	--	44.8
Initial Spares	--	--	--	147.4	--	--	163.8
MILCON	0.0	0.0	--	0.0	0.0	0.0	0.0
Acq O&M	0.0	0.0	--	0.0	0.0	0.0	0.0
Total	1824.8	3031.0	N/A	3872.3	1818.9	3336.2	4492.7

¹ APB Breach

Confidence Level

Confidence Level of cost estimate for current APB: 47%

The MIDS cost model is built using Microsoft Excel 2010. Total Life Cycle Cost Estimate (LCCE) for MIDS is at the 47% confidence level on the generated Sigmoid (S)-Curve. The generated point estimate is based on the developed Cost Estimating Relationships (CERs) and inputted sunk costs rather than an estimate at a chosen confidence level. MIDS has incorporated the actual costs of our most recent development of MIDS Joint Tactical Radio System (MIDS JTRS) Phase 2B to build in more confidence and validate the confidence level.

Cost Notes

RDT&E costs include the MIDS Low Volume Terminal (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS) terminal development, terminal acquisition, integration and test on the United States Navy platforms for all current MIDS Program Management Office enhancement efforts.

Procurement costs are for MIDS-LVT and MIDS JTRS terminals purchased by the platforms.

The costs of platform installation and platform kits, and United States Air Force and United States Army platform integration and testing of MIDS-LVT and MIDS JTRS are to be included in the respective budgets and baseline agreements of the various platforms implementing MIDS.

The current production terminal procurement estimate increased by a total of 2,149 terminals due to the procurement order from the U.S. Air Force (Platforms: F-15, F-16, F-22).

Total Quantity			
Quantity	SAR Baseline Production Estimate	Current APB Production	Current Estimate
RDT&E	143	488	604
Procurement	2821	5745	8000
Total	2964	6233	8604

Quantity Notes

The unit of measure is terminals.

Procurement quantities include MIDS terminals for United States Navy, United States Air Force, and United States Army platforms. The current estimate includes MIDS Joint Tactical Radio System (MIDS JTRS) procurement quantities for the Phase 2B Core terminals, Four Net Concurrent Multi-Netting with Concurrent Contention Receive (CMN-4), and Tactical Targeting Network Technology (TTNT).

Procurement budgets include funding to upgrade terminals, e.g. make a Core terminal CMN-4 capable, CMN-4 to TTNT, and MIDS-LVT to BU2. However, these terminals are not included in future quantity counts as they have already been accounted for when they were initially procured.

The current production terminal procurement estimate increased by a total of 2,149 terminals due to the procurement order from the U.S. Air Force (Platforms: F-15, F-16, F-22) and the U.S. Navy.

Cost and Funding

Funding Summary

Appropriation Summary									
FY 2017 President's Budget / December 2015 SAR (TY\$ M)									
Appropriation	Prior	FY 2016	FY 2017	FY 2018	FY 2019	FY 2020	FY 2021	To Complete	Total
RDT&E	1670.4	73.7	57.4	21.1	17.8	18.1	18.5	0.0	1877.0
Procurement	1403.8	100.9	155.2	223.4	252.0	195.3	115.1	170.0	2615.7
MILCON	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Acq O&M	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
PB 2017 Total	3074.2	174.6	212.6	244.5	269.8	213.4	133.6	170.0	4492.7
PB 2016 Total	2999.2	137.4	137.6	119.5	80.8	71.6	0.0	0.0	3546.1
Delta	75.0	37.2	75.0	125.0	189.0	141.8	133.6	170.0	946.6

Quantity Summary										
FY 2017 President's Budget / December 2015 SAR (TY\$ M)										
Quantity	Undistributed	Prior	FY 2016	FY 2017	FY 2018	FY 2019	FY 2020	FY 2021	To Complete	Total
Development	604	0	0	0	0	0	0	0	0	604
Production	0	5063	320	438	688	744	432	133	182	8000
PB 2017 Total	604	5063	320	438	688	744	432	133	182	8604
PB 2016 Total	548	4941	203	176	232	157	142	0	0	6399
Delta	56	122	117	262	456	587	290	133	182	2205

Cost and Funding

Annual Funding By Appropriation

Annual Funding							
0400 RDT&E Research, Development, Test, and Evaluation, Defense-Wide							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1990	--	--	--	--	--	--	9.0
1991	--	--	--	--	--	--	5.0
1992	--	--	--	--	--	--	16.5
1993	--	--	--	--	--	--	23.9
1994	--	--	--	--	--	--	23.3
1995	--	--	--	--	--	--	49.6
1996	--	--	--	--	--	--	42.7
1997	--	--	--	--	--	--	36.9
1998	--	--	--	--	--	--	45.2
1999	--	--	--	--	--	--	27.9
2000	--	--	--	--	--	--	39.0
2001	--	--	--	--	--	--	12.0
2002	--	--	--	--	--	--	13.1
2003	--	--	--	--	--	--	7.7
2004	--	--	--	--	--	--	7.0
2005	--	--	--	--	--	--	9.6
2006	--	--	--	--	--	--	1.0
2007	--	--	--	--	--	--	2.0
2008	--	--	--	--	--	--	--
2009	--	--	--	--	--	--	0.8
2010	--	--	--	--	--	--	--
2011	--	--	--	--	--	--	0.2
2012	--	--	--	--	--	--	--
2013	--	--	--	--	--	--	0.3
Subtotal	70	--	--	--	--	--	372.7

Annual Funding							
0400 RDT&E Research, Development, Test, and Evaluation, Defense-Wide							
Fiscal Year	Quantity	BY 2003 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1990	--	--	--	--	--	--	11.1
1991	--	--	--	--	--	--	5.9
1992	--	--	--	--	--	--	19.1
1993	--	--	--	--	--	--	27.2
1994	--	--	--	--	--	--	26.0
1995	--	--	--	--	--	--	54.3
1996	--	--	--	--	--	--	45.9
1997	--	--	--	--	--	--	39.2
1998	--	--	--	--	--	--	47.6
1999	--	--	--	--	--	--	29.0
2000	--	--	--	--	--	--	40.0
2001	--	--	--	--	--	--	12.1
2002	--	--	--	--	--	--	13.1
2003	--	--	--	--	--	--	7.6
2004	--	--	--	--	--	--	6.7
2005	--	--	--	--	--	--	9.0
2006	--	--	--	--	--	--	0.9
2007	--	--	--	--	--	--	1.8
2008	--	--	--	--	--	--	--
2009	--	--	--	--	--	--	0.7
2010	--	--	--	--	--	--	--
2011	--	--	--	--	--	--	0.2
2012	--	--	--	--	--	--	--
2013	--	--	--	--	--	--	0.2
Subtotal	70	--	--	--	--	--	397.6

Annual Funding							
1319 RDT&E Research, Development, Test, and Evaluation, Navy							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1990	--	--	--	--	--	--	2.9
1991	--	--	--	--	--	--	4.7
1992	--	--	--	--	--	--	10.0
1993	--	--	--	--	--	--	12.4
1994	--	--	--	--	--	--	23.0
1995	--	--	--	--	--	--	18.4
1996	--	--	--	--	--	--	31.0
1997	--	--	--	--	--	--	28.2
1998	--	--	--	--	--	--	39.8
1999	--	--	--	--	--	--	45.4
2000	--	--	--	--	--	--	62.3
2001	--	--	--	--	--	--	37.7
2002	--	--	--	--	--	--	26.2
2003	--	--	--	--	--	--	16.8
2004	--	--	--	--	--	--	22.4
2005	--	--	--	--	--	--	27.6
2006	--	--	--	--	--	--	98.2
2007	--	--	--	--	--	--	162.5
2008	--	--	--	--	--	--	77.2
2009	--	--	--	--	--	--	26.6
2010	--	--	--	--	--	--	16.2
2011	--	--	--	--	--	--	24.2
2012	--	--	--	--	--	--	100.8
2013	--	--	--	--	--	--	47.2
2014	--	--	--	--	--	--	120.7
2015	--	--	--	--	--	--	80.5
2016	--	--	--	--	--	--	70.2
2017	--	--	--	--	--	--	57.4
2018	--	--	--	--	--	--	21.1
2019	--	--	--	--	--	--	17.8
2020	--	--	--	--	--	--	18.1
2021	--	--	--	--	--	--	18.5
Subtotal	202	--	--	--	--	--	1366.0

Annual Funding							
1319 RDT&E Research, Development, Test, and Evaluation, Navy							
Fiscal Year	Quantity	BY 2003 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1990	--	--	--	--	--	--	3.6
1991	--	--	--	--	--	--	5.6
1992	--	--	--	--	--	--	11.6
1993	--	--	--	--	--	--	14.1
1994	--	--	--	--	--	--	25.6
1995	--	--	--	--	--	--	20.1
1996	--	--	--	--	--	--	33.3
1997	--	--	--	--	--	--	30.0
1998	--	--	--	--	--	--	41.9
1999	--	--	--	--	--	--	47.3
2000	--	--	--	--	--	--	63.9
2001	--	--	--	--	--	--	38.2
2002	--	--	--	--	--	--	26.3
2003	--	--	--	--	--	--	16.6
2004	--	--	--	--	--	--	21.5
2005	--	--	--	--	--	--	25.8
2006	--	--	--	--	--	--	89.2
2007	--	--	--	--	--	--	144.0
2008	--	--	--	--	--	--	67.2
2009	--	--	--	--	--	--	22.9
2010	--	--	--	--	--	--	13.7
2011	--	--	--	--	--	--	20.0
2012	--	--	--	--	--	--	82.0
2013	--	--	--	--	--	--	38.0
2014	--	--	--	--	--	--	95.8
2015	--	--	--	--	--	--	63.1
2016	--	--	--	--	--	--	54.1
2017	--	--	--	--	--	--	43.5
2018	--	--	--	--	--	--	15.7
2019	--	--	--	--	--	--	13.0
2020	--	--	--	--	--	--	12.9
2021	--	--	--	--	--	--	13.0
Subtotal	202	--	--	--	--	--	1213.5

Annual Funding							
2040 RDT&E Research, Development, Test, and Evaluation, Army							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1997	--	--	--	--	--	--	0.5
1998	--	--	--	--	--	--	2.4
1999	--	--	--	--	--	--	5.2
2000	--	--	--	--	--	--	--
2001	--	--	--	--	--	--	0.1
2002	--	--	--	--	--	--	3.1
2003	--	--	--	--	--	--	0.6
2004	--	--	--	--	--	--	3.1
2005	--	--	--	--	--	--	4.4
2006	--	--	--	--	--	--	--
2007	--	--	--	--	--	--	1.5
2008	--	--	--	--	--	--	1.9
2009	--	--	--	--	--	--	3.3
2010	--	--	--	--	--	--	0.2
2011	--	--	--	--	--	--	--
2012	--	--	--	--	--	--	0.2
2013	--	--	--	--	--	--	0.4
2014	--	--	--	--	--	--	0.2
Subtotal	78	--	--	--	--	--	27.1

Annual Funding 2040 RDT&E Research, Development, Test, and Evaluation, Army							
Fiscal Year	Quantity	BY 2003 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1997	--	--	--	--	--	--	0.5
1998	--	--	--	--	--	--	2.5
1999	--	--	--	--	--	--	5.4
2000	--	--	--	--	--	--	--
2001	--	--	--	--	--	--	0.1
2002	--	--	--	--	--	--	3.1
2003	--	--	--	--	--	--	0.6
2004	--	--	--	--	--	--	3.0
2005	--	--	--	--	--	--	4.1
2006	--	--	--	--	--	--	--
2007	--	--	--	--	--	--	1.3
2008	--	--	--	--	--	--	1.6
2009	--	--	--	--	--	--	2.8
2010	--	--	--	--	--	--	0.2
2011	--	--	--	--	--	--	--
2012	--	--	--	--	--	--	0.2
2013	--	--	--	--	--	--	0.3
2014	--	--	--	--	--	--	0.2
Subtotal	78	--	--	--	--	--	25.9

Annual Funding							
3600 RDT&E Research, Development, Test, and Evaluation, Air Force							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1997	--	--	--	--	--	--	3.9
1998	--	--	--	--	--	--	8.0
1999	--	--	--	--	--	--	0.2
2000	--	--	--	--	--	--	6.3
2001	--	--	--	--	--	--	3.9
2002	--	--	--	--	--	--	2.9
2003	--	--	--	--	--	--	4.3
2004	--	--	--	--	--	--	14.3
2005	--	--	--	--	--	--	19.6
2006	--	--	--	--	--	--	4.5
2007	--	--	--	--	--	--	2.2
2008	--	--	--	--	--	--	1.4
2009	--	--	--	--	--	--	5.7
2010	--	--	--	--	--	--	1.5
2011	--	--	--	--	--	--	2.4
2012	--	--	--	--	--	--	2.2
2013	--	--	--	--	--	--	3.6
2014	--	--	--	--	--	--	2.6
2015	--	--	--	--	--	--	18.2
2016	--	--	--	--	--	--	3.5
Subtotal	254	--	--	--	--	--	111.2

Annual Funding 3600 RDT&E Research, Development, Test, and Evaluation, Air Force							
Fiscal Year	Quantity	BY 2003 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1997	--	--	--	--	--	--	4.1
1998	--	--	--	--	--	--	8.4
1999	--	--	--	--	--	--	0.2
2000	--	--	--	--	--	--	6.5
2001	--	--	--	--	--	--	3.9
2002	--	--	--	--	--	--	2.9
2003	--	--	--	--	--	--	4.3
2004	--	--	--	--	--	--	13.8
2005	--	--	--	--	--	--	18.4
2006	--	--	--	--	--	--	4.1
2007	--	--	--	--	--	--	2.0
2008	--	--	--	--	--	--	1.2
2009	--	--	--	--	--	--	4.9
2010	--	--	--	--	--	--	1.3
2011	--	--	--	--	--	--	2.0
2012	--	--	--	--	--	--	1.8
2013	--	--	--	--	--	--	2.9
2014	--	--	--	--	--	--	2.1
2015	--	--	--	--	--	--	14.3
2016	--	--	--	--	--	--	2.7
Subtotal	254	--	--	--	--	--	101.8

Annual Funding 0300 Procurement Procurement, Defense-Wide							
Fiscal Year	Quantity	TY \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1999	11	2.7	0.1	4.5	7.3	0.6	7.9
2000	--	--	--	--	--	--	--
2001	19	4.8	0.1	--	4.9	1.0	5.9
2002	--	--	--	--	--	0.3	0.3
2003	10	2.5	--	--	2.5	0.1	2.6
2004	--	--	--	--	--	--	--
2005	4	1.0	--	--	1.0	--	1.0
2006	--	--	--	--	--	--	--
2007	--	--	--	--	--	--	--
2008	--	--	--	--	--	--	--
2009	--	--	--	--	--	--	--
2010	7	1.5	--	--	1.5	--	1.5
2011	5	1.1	--	--	1.1	--	1.1
2012	--	--	--	--	--	--	--
2013	--	--	--	--	--	--	--
2014	2	0.5	--	--	0.5	--	0.5
Subtotal	58	14.1	0.2	4.5	18.8	2.0	20.8

Annual Funding 0300 Procurement Procurement, Defense-Wide								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1999	11	2.8	0.1	4.7	7.6	0.6	8.2	
2000	--	--	--	--	--	--	--	
2001	19	4.8	0.1	--	4.9	1.0	5.9	
2002	--	--	--	--	--	0.3	0.3	
2003	10	2.4	--	--	2.4	0.1	2.5	
2004	--	--	--	--	--	--	--	
2005	4	0.9	--	--	0.9	--	0.9	
2006	--	--	--	--	--	--	--	
2007	--	--	--	--	--	--	--	
2008	--	--	--	--	--	--	--	
2009	--	--	--	--	--	--	--	
2010	7	1.3	--	--	1.3	--	1.3	
2011	5	0.9	--	--	0.9	--	0.9	
2012	--	--	--	--	--	--	--	
2013	--	--	--	--	--	--	--	
2014	2	0.4	--	--	0.4	--	0.4	
Subtotal	58	13.5	0.2	4.7	18.4	2.0	20.4	

This appropriation provides for the procurement of the Army unique MIDS Low Volume Terminal (MIDS-LVT) (2) and MIDS-LVT (11) variants for the Patriot Air Defense System, THAAD and GAPO. There was an overall decrease in this appropriation due to the Army GAPO de-obligating 2 terminals since the previous SAR.

Annual Funding 1506 Procurement Aircraft Procurement, Navy								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1999	16	5.9	1.3	0.5	7.7	0.3	8.0	
2000	58	15.1	1.8	35.5	52.4	8.3	60.7	
2001	64	20.2	3.7	0.2	24.1	2.5	26.6	
2002	103	23.9	0.5	--	24.4	10.6	35.0	
2003	116	22.7	3.6	--	26.3	10.4	36.7	
2004	138	27.8	3.2	--	31.0	8.4	39.4	
2005	130	25.7	2.9	--	28.6	13.8	42.4	
2006	169	31.0	2.9	0.1	34.0	1.8	35.8	
2007	169	35.2	3.0	--	38.2	5.2	43.4	
2008	202	40.4	2.9	--	43.3	9.4	52.7	
2009	127	28.5	2.9	--	31.4	1.0	32.4	
2010	174	29.9	0.2	--	30.1	3.9	34.0	
2011	147	29.1	0.2	--	29.3	3.9	33.2	
2012	128	31.6	0.2	--	31.8	7.5	39.3	
2013	262	74.8	0.2	--	75.0	--	75.0	
2014	176	48.5	0.2	--	48.7	2.5	51.2	
2015	62	13.6	0.2	--	13.8	7.2	21.0	
2016	215	57.3	0.2	--	57.5	5.7	63.2	
2017	235	65.1	0.2	--	65.3	7.1	72.4	
2018	268	76.6	0.2	--	76.8	4.1	80.9	
2019	190	63.6	0.2	--	63.8	2.7	66.5	
2020	154	93.2	0.2	--	93.4	2.9	96.3	
2021	86	86.8	0.2	--	87.0	1.6	88.6	
2022	78	78.5	0.2	--	78.7	--	78.7	
2023	43	63.8	--	--	63.8	--	63.8	
Subtotal	3510	1088.8	31.3	36.3	1156.4	120.8	1277.2	

Annual Funding 1506 Procurement Aircraft Procurement, Navy								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1999	16	6.1	1.3	0.5	7.9	0.3	8.2	
2000	58	15.3	1.8	36.1	53.2	8.4	61.6	
2001	64	20.2	3.8	0.2	24.2	2.5	26.7	
2002	103	23.7	0.5	--	24.2	10.4	34.6	
2003	116	22.0	3.5	--	25.5	10.1	35.6	
2004	138	26.3	3.0	--	29.3	8.0	37.3	
2005	130	23.6	2.7	--	26.3	12.7	39.0	
2006	169	27.7	2.6	0.1	30.4	1.6	32.0	
2007	169	30.8	2.6	--	33.4	4.5	37.9	
2008	202	34.8	2.5	--	37.3	8.1	45.4	
2009	127	24.2	2.5	--	26.7	0.8	27.5	
2010	174	24.9	0.2	--	25.1	3.2	28.3	
2011	147	23.7	0.2	--	23.9	3.2	27.1	
2012	128	25.4	0.2	--	25.6	6.0	31.6	
2013	262	59.5	0.2	--	59.7	--	59.7	
2014	176	38.1	0.2	--	38.3	1.9	40.2	
2015	62	10.5	0.2	--	10.7	5.6	16.3	
2016	215	43.6	0.2	--	43.8	4.3	48.1	
2017	235	48.6	0.1	--	48.7	5.4	54.1	
2018	268	56.1	0.1	--	56.2	3.0	59.2	
2019	190	45.7	0.1	--	45.8	1.9	47.7	
2020	154	65.6	0.1	--	65.7	2.1	67.8	
2021	86	59.9	0.1	--	60.0	1.1	61.1	
2022	78	53.1	0.1	--	53.2	--	53.2	
2023	43	42.3	--	--	42.3	--	42.3	
Subtotal	3510	851.7	28.8	36.9	917.4	105.1	1022.5	

This appropriation identifies the MIDS Low Volume Terminal (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS) core, CMN4 and TTNT that are planned for the Navy F/A-18C/D/E/F, E/A-18G, E-2D, P-3, P-8, KC-130, EP-3E, MH-60R/S, the EA-6B.

This appropriation increased by 72 MIDS-LVT terminals and 403 MIDS JTRS terminals since the previous SAR.

Annual Funding 1611 Procurement Shipbuilding and Conversion, Navy								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	1	0.4	--	--	0.4	--	0.4	
2002	2	0.9	--	--	0.9	--	0.9	
2003	5	2.1	--	--	2.1	--	2.1	
2004	5	0.9	--	--	0.9	--	0.9	
2005	3	0.7	--	--	0.7	--	0.7	
2006	4	0.7	--	--	0.7	--	0.7	
2007	--	--	--	--	--	--	--	
2008	2	0.4	--	--	0.4	--	0.4	
2009	2	0.4	--	--	0.4	--	0.4	
2010	4	0.7	--	--	0.7	--	0.7	
2011	8	1.4	--	--	1.4	--	1.4	
2012	7	1.3	--	--	1.3	--	1.3	
2013	5	0.9	--	--	0.9	--	0.9	
2014	5	0.9	--	--	0.9	--	0.9	
2015	3	0.5	--	--	0.5	--	0.5	
2016	3	0.7	--	--	0.7	--	0.7	
2017	8	2.3	--	--	2.3	--	2.3	
2018	3	1.1	--	--	1.1	--	1.1	
2019	4	2.8	--	--	2.8	--	2.8	
2020	5	5.3	--	--	5.3	--	5.3	
2021	4	4.3	--	--	4.3	--	4.3	
2022	1	2.6	--	--	2.6	--	2.6	
2023	1	2.2	--	--	2.2	--	2.2	
Subtotal	85	33.5	--	--	33.5	--	33.5	

Annual Funding 1611 Procurement Shipbuilding and Conversion, Navy								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	1	0.4	--	--	0.4	--	0.4	
2002	2	0.9	--	--	0.9	--	0.9	
2003	5	1.9	--	--	1.9	--	1.9	
2004	5	0.8	--	--	0.8	--	0.8	
2005	3	0.6	--	--	0.6	--	0.6	
2006	4	0.6	--	--	0.6	--	0.6	
2007	--	--	--	--	--	--	--	
2008	2	0.3	--	--	0.3	--	0.3	
2009	2	0.3	--	--	0.3	--	0.3	
2010	4	0.5	--	--	0.5	--	0.5	
2011	8	0.9	--	--	0.9	--	0.9	
2012	7	0.9	--	--	0.9	--	0.9	
2013	5	0.6	--	--	0.6	--	0.6	
2014	5	0.6	--	--	0.6	--	0.6	
2015	3	0.3	--	--	0.3	--	0.3	
2016	3	0.4	--	--	0.4	--	0.4	
2017	8	1.4	--	--	1.4	--	1.4	
2018	3	0.7	--	--	0.7	--	0.7	
2019	4	1.6	--	--	1.6	--	1.6	
2020	5	3.0	--	--	3.0	--	3.0	
2021	4	2.4	--	--	2.4	--	2.4	
2022	1	1.4	--	--	1.4	--	1.4	
2023	1	1.2	--	--	1.2	--	1.2	
Subtotal	85	21.7	--	--	21.7	--	21.7	

This appropriation identifies the MIDS on Ship variant for new construction surface ships. This appropriation increased by 6 MIDS-LVT terminals and 26 MIDS JTRS terminals since the previous SAR.

Annual Funding 1810 Procurement Other Procurement, Navy								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1999	3	1.1	--	--	1.1	--	1.1	
2000	--	--	--	--	--	--	--	
2001	--	--	--	--	--	--	--	
2002	2	0.5	--	--	0.5	--	0.5	
2003	6	1.7	--	--	1.7	--	1.7	
2004	8	1.8	--	--	1.8	--	1.8	
2005	--	--	--	--	--	0.1	0.1	
2006	8	1.9	--	0.1	2.0	--	2.0	
2007	17	3.8	--	--	3.8	0.6	4.4	
2008	26	6.6	--	--	6.6	--	6.6	
2009	6	1.2	--	--	1.2	--	1.2	
2010	12	2.5	--	--	2.5	--	2.5	
2011	44	9.8	--	--	9.8	--	9.8	
2012	6	1.2	--	--	1.2	--	1.2	
2013	26	7.0	--	--	7.0	--	7.0	
2014	6	1.3	--	--	1.3	--	1.3	
2015	15	2.8	--	--	2.8	--	2.8	
2016	30	8.0	--	--	8.0	--	8.0	
2017	35	9.3	--	--	9.3	--	9.3	
2018	27	9.3	--	--	9.3	--	9.3	
2019	15	11.4	--	--	11.4	--	11.4	
2020	15	9.5	--	--	9.5	--	9.5	
2021	5	4.2	--	--	4.2	--	4.2	
2022	1	4.9	--	--	4.9	--	4.9	
Subtotal	313	99.8	--	0.1	99.9	0.7	100.6	

Annual Funding 1810 Procurement Other Procurement, Navy								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1999	3	1.1	--	--	1.1	--	1.1	
2000	--	--	--	--	--	--	--	
2001	--	--	--	--	--	--	--	
2002	2	0.5	--	--	0.5	--	0.5	
2003	6	1.7	--	--	1.7	--	1.7	
2004	8	1.7	--	--	1.7	--	1.7	
2005	--	--	--	--	--	0.1	0.1	
2006	8	1.7	--	0.1	1.8	--	1.8	
2007	17	3.3	--	--	3.3	0.6	3.9	
2008	26	5.7	--	--	5.7	--	5.7	
2009	6	1.0	--	--	1.0	--	1.0	
2010	12	2.1	--	--	2.1	--	2.1	
2011	44	8.1	--	--	8.1	--	8.1	
2012	6	1.0	--	--	1.0	--	1.0	
2013	26	5.6	--	--	5.6	--	5.6	
2014	6	1.0	--	--	1.0	--	1.0	
2015	15	2.2	--	--	2.2	--	2.2	
2016	30	6.1	--	--	6.1	--	6.1	
2017	35	7.0	--	--	7.0	--	7.0	
2018	27	6.8	--	--	6.8	--	6.8	
2019	15	8.2	--	--	8.2	--	8.2	
2020	15	6.7	--	--	6.7	--	6.7	
2021	5	2.9	--	--	2.9	--	2.9	
2022	1	3.3	--	--	3.3	--	3.3	
Subtotal	313	77.7	--	0.1	77.8	0.7	78.5	

This appropriation increased by 57 MIDS-Low Volume Terminal (MIDS-LVT) terminals and 107 MIDS Joint Tactical Radio System (JTRS) terminals since the previous SAR.

Annual Funding								
2035 Procurement Other Procurement, Army								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	1	0.3	--	--	0.3	--	0.3	
2002	--	--	--	--	--	--	--	
2003	4	1.0	--	--	1.0	0.4	1.4	
2004	5	1.3	--	--	1.3	0.4	1.7	
2005	62	15.7	--	--	15.7	1.2	16.9	
2006	67	16.3	--	--	16.3	0.1	16.4	
2007	40	9.4	--	--	9.4	1.1	10.5	
2008	144	33.5	--	--	33.5	--	33.5	
2009	29	6.4	--	--	6.4	2.2	8.6	
2010	30	7.0	--	--	7.0	1.6	8.6	
2011	22	4.8	--	--	4.8	1.0	5.8	
2012	9	2.0	--	--	2.0	0.1	2.1	
2013	5	3.3	--	--	3.3	0.4	3.7	
2014	1	1.1	--	--	1.1	0.1	1.2	
2015	2	0.1	--	--	0.1	3.9	4.0	
2016	1	9.4	--	--	9.4	--	9.4	
2017	1	12.4	--	--	12.4	--	12.4	
2018	1	12.4	--	--	12.4	--	12.4	
2019	1	11.4	--	--	11.4	--	11.4	
2020	1	5.5	--	--	5.5	--	5.5	
2021	1	6.5	--	--	6.5	--	6.5	
Subtotal	427	159.8	--	--	159.8	12.5	172.3	

Annual Funding 2035 Procurement Other Procurement, Army								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	1	0.3	--	--	0.3	--	0.3	
2002	--	--	--	--	--	--	--	
2003	4	1.0	--	--	1.0	0.4	1.4	
2004	5	1.2	--	--	1.2	0.4	1.6	
2005	62	14.5	--	--	14.5	1.1	15.6	
2006	67	14.7	--	--	14.7	0.1	14.8	
2007	40	8.3	--	--	8.3	0.9	9.2	
2008	144	29.0	--	--	29.0	--	29.0	
2009	29	5.5	--	--	5.5	1.8	7.3	
2010	30	5.9	--	--	5.9	1.3	7.2	
2011	22	4.0	--	--	4.0	0.8	4.8	
2012	9	1.6	--	--	1.6	0.1	1.7	
2013	5	2.6	--	--	2.6	0.3	2.9	
2014	1	0.9	--	--	0.9	--	0.9	
2015	2	0.1	--	--	0.1	3.0	3.1	
2016	1	7.2	--	--	7.2	--	7.2	
2017	1	9.3	--	--	9.3	--	9.3	
2018	1	9.1	--	--	9.1	--	9.1	
2019	1	8.2	--	--	8.2	--	8.2	
2020	1	3.9	--	--	3.9	--	3.9	
2021	1	4.5	--	--	4.5	--	4.5	
Subtotal	427	131.8	--	--	131.8	10.2	142.0	

This appropriation provides for the procurement of the Army unique MIDS Low Volume Terminal (MIDS-LVT) (2) and MIDS-LVT (11) variants. This appropriation increased by 2 MIDS-LVT terminals since the previous SAR.

Annual Funding								
3010 Procurement Aircraft Procurement, Air Force								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	52	8.5	--	4.4	12.9	6.9	19.8	
2002	150	32.5	--	--	32.5	10.2	42.7	
2003	180	36.8	--	--	36.8	10.5	47.3	
2004	137	24.3	--	--	24.3	13.8	38.1	
2005	164	35.5	--	0.1	35.6	4.3	39.9	
2006	129	25.1	--	--	25.1	1.7	26.8	
2007	152	31.1	--	--	31.1	3.4	34.5	
2008	52	14.7	--	--	14.7	4.4	19.1	
2009	15	5.0	--	--	5.0	1.6	6.6	
2010	51	13.0	--	--	13.0	2.4	15.4	
2011	34	9.5	--	--	9.5	0.2	9.7	
2012	83	25.8	--	--	25.8	--	25.8	
2013	43	11.3	--	--	11.3	--	11.3	
2014	34	11.7	--	--	11.7	--	11.7	
2015	1	5.8	--	--	5.8	--	5.8	
2016	65	17.8	--	--	17.8	--	17.8	
2017	148	46.4	--	--	46.4	--	46.4	
2018	377	109.4	--	--	109.4	--	109.4	
2019	522	153.3	--	--	153.3	--	153.3	
2020	233	72.7	--	--	72.7	--	72.7	
2021	37	11.5	--	--	11.5	--	11.5	
2022	23	7.0	--	--	7.0	--	7.0	
2023	13	3.9	--	--	3.9	--	3.9	
2024	22	6.9	--	--	6.9	--	6.9	
Subtotal	2717	719.5	--	4.5	724.0	59.4	783.4	

Annual Funding								
3010 Procurement Aircraft Procurement, Air Force								
Fiscal Year	Quantity	BY 2003 \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
2001	52	8.5	--	4.4	12.9	6.9	19.8	
2002	150	32.2	--	--	32.2	10.1	42.3	
2003	180	35.9	--	--	35.9	10.2	46.1	
2004	137	23.1	--	--	23.1	13.1	36.2	
2005	164	32.7	--	0.1	32.8	4.0	36.8	
2006	129	22.6	--	--	22.6	1.5	24.1	
2007	152	27.2	--	--	27.2	3.0	30.2	
2008	52	12.7	--	--	12.7	3.7	16.4	
2009	15	4.2	--	--	4.2	1.4	5.6	
2010	51	10.8	--	--	10.8	2.0	12.8	
2011	34	7.8	--	--	7.8	0.1	7.9	
2012	83	20.8	--	--	20.8	--	20.8	
2013	43	8.9	--	--	8.9	--	8.9	
2014	34	9.1	--	--	9.1	--	9.1	
2015	1	4.5	--	--	4.5	--	4.5	
2016	65	13.4	--	--	13.4	--	13.4	
2017	148	34.3	--	--	34.3	--	34.3	
2018	377	79.4	--	--	79.4	--	79.4	
2019	522	109.1	--	--	109.1	--	109.1	
2020	233	50.7	--	--	50.7	--	50.7	
2021	37	7.9	--	--	7.9	--	7.9	
2022	23	4.7	--	--	4.7	--	4.7	
2023	13	2.6	--	--	2.6	--	2.6	
2024	22	4.4	--	--	4.4	--	4.4	
Subtotal	2717	567.5	--	4.5	572.0	56.0	628.0	

This appropriation identifies the MIDS Low Volume Terminal (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS) terminals that are planned for the F-15, F-22, F-16, AC-130, RC-135, EC130E/H, B-1, E-8C, the Airborne Laser and United States Air Force shore sites. This appropriation increased by 67 MIDS-LVT terminals and 1346 MIDS JTRS terminals since the previous SAR.

Annual Funding								
3080 Procurement Other Procurement, Air Force								
Fiscal Year	Quantity	TY \$M						
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program	
1996	6	3.0	--	--	3.0	--	3.0	
1997	--	--	--	0.3	0.3	--	0.3	
1998	77	18.5	--	15.2	33.7	1.0	34.7	
1999	173	33.0	0.3	--	33.3	2.1	35.4	
2000	294	49.8	0.7	0.5	51.0	3.8	54.8	
2001	148	26.7	0.6	4.4	31.7	1.0	32.7	
2002	97	18.6	--	5.6	24.2	--	24.2	
2003	30	0.4	--	--	0.4	5.3	5.7	
2004	--	--	--	--	--	--	--	
2005	--	--	--	--	--	--	--	
2006	--	--	--	--	--	--	--	
2007	--	--	--	--	--	--	--	
2008	--	--	--	--	--	--	--	
2009	--	--	--	--	--	--	--	
2010	--	--	--	--	--	--	--	
2011	--	--	--	--	--	--	--	
2012	--	--	--	--	--	--	--	
2013	--	--	--	--	--	--	--	
2014	--	--	--	--	--	--	--	
2015	--	--	--	--	--	--	--	
2016	6	1.8	--	--	1.8	--	1.8	
2017	11	12.4	--	--	12.4	--	12.4	
2018	12	10.3	--	--	10.3	--	10.3	
2019	12	6.6	--	--	6.6	--	6.6	
2020	24	6.0	--	--	6.0	--	6.0	
Subtotal	890	187.1	1.6	26.0	214.7	13.2	227.9	

Annual Funding 3080 Procurement Other Procurement, Air Force							
Fiscal Year	Quantity	BY 2003 \$M					
		End Item Recurring Flyaway	Non End Item Recurring Flyaway	Non Recurring Flyaway	Total Flyaway	Total Support	Total Program
1996	6	3.2	--	--	3.2	--	3.2
1997	--	--	--	0.3	0.3	--	0.3
1998	77	19.2	--	15.7	34.9	1.0	35.9
1999	173	33.8	0.3	--	34.1	2.2	36.3
2000	294	50.3	0.7	0.5	51.5	3.8	55.3
2001	148	26.5	0.6	4.4	31.5	1.0	32.5
2002	97	18.2	--	5.4	23.6	--	23.6
2003	30	0.4	--	--	0.4	5.2	5.6
2004	--	--	--	--	--	--	--
2005	--	--	--	--	--	--	--
2006	--	--	--	--	--	--	--
2007	--	--	--	--	--	--	--
2008	--	--	--	--	--	--	--
2009	--	--	--	--	--	--	--
2010	--	--	--	--	--	--	--
2011	--	--	--	--	--	--	--
2012	--	--	--	--	--	--	--
2013	--	--	--	--	--	--	--
2014	--	--	--	--	--	--	--
2015	--	--	--	--	--	--	--
2016	6	1.4	--	--	1.4	--	1.4
2017	11	9.5	--	--	9.5	--	9.5
2018	12	7.7	--	--	7.7	--	7.7
2019	12	4.8	--	--	4.8	--	4.8
2020	24	4.3	--	--	4.3	--	4.3
Subtotal	890	179.3	1.6	26.3	207.2	13.2	220.4

This appropriation identifies the MIDS Fighter Data Link (FDL) terminals for the F-15C/D/E that are being procured on a separate contract. The FY 1996 funding (TY \$3.0M) reports the United States Air Force funds contributed to the qualification and build of six FDL terminals. Additional funds in excess of \$8.0M were contributed by the contractor, Data Link Solutions L.L.C., for completion of the full qualification program requirements.

This appropriation also includes the MIDS-Low Volume Terminal (MIDS-LVT) procurement for the Air Force. This appropriation increased by 65 MIDS-LVT terminals since the previous SAR.

Low Rate Initial Production

Item	Initial LRIP Decision	Current Total LRIP
Approval Date	5/11/2000	12/8/2003
Approved Quantity	70	544
Reference	Milestone II ADM	Milestone C ADM
Start Year	2000	2000
End Year	2001	2003

The MDA authorized LRIP on May 11, 2000 for 70 MIDS Low Volume Terminal (MIDS-LVT). Three additional LRIP decisions were authorized for a cumulative total of 544 MIDS-LVT and MIDS-LVT(2) variants (about 25 percent of the then planned procurement of 2,145 terminals). Based on a Milestone C decision in 2003 for the MIDS program, USD (AT&L) General Counsel and senior staff changed the title of the 2009 DAB decision for MIDS JTRS to Limited Production and Fielding (LP&F). A follow-on decision for the MIDS JTRS variant was made for Full Production and Fielding (FP&F), and not FRP. On December 23, 2009 an ADM approved the award of the limited production of 41 MIDS JTRS variant terminals to support the F/A-18E/F production schedule and Joint Surveillance Target Attack Radar System (JSTARS) integration and testing requirements. On January 31, 2011, an ADM approved an award of a second limited production for 42 MIDS JTRS variant terminals to support F/A-18E/F production, RC-135 Rivet Joint, EC-130H Compass Call, and other Service requirements.

Foreign Military Sales

Country	Date of Sale	Quantity	Total Cost \$M	Description
Kuwait	9/24/2015	4	0.9	Date of sale listed is the most current buy on FMS case KU-B-UMG.
Netherlands	9/24/2015	10	5.4	Total Costs are cumulative over multiple years and FMS cases (NE-P-LFT; NE-P-LGT). Date of sale listed is the most current buy.
Australia	9/18/2015	271	60.4	Total Costs are cumulative over multiple years and FMS cases (AT-D-QCI; AT-P-GOV; AT-P-LAB; AT-P-LCE; AT-P-LCK; AT-P-LCQ; AT-P-LDN; AT-P-LER; AT-P-LET; AT-P-SAF; AT-P-SCF; AT-P-SCI; AT-P-LFA). Date of sale listed is the most current buy.
United Kingdom	9/18/2015	10	3.2	Total Costs are cumulative over multiple years and FMS cases (UK-D-SAO; UK-P-LVE). Date of sale listed is the most current buy.
Oman	8/31/2015	72	13.7	Total Costs are cumulative over multiple years and FMS cases (MU-D-SAB; MU-P-LAP). Date of sale listed is the most current buy.
Romania	8/31/2015	15	2.7	Total Cost is cumulative over multiple years. Date of sale listed is the most current buy on FMS case RO-D-QAH.
Thailand	8/31/2015	24	4.5	Total Costs are cumulative over multiple years and FMS cases (TH-D-QCZ; TH-P-LFA). Date of sale listed is the most current buy.
Singapore	3/6/2015	61	7.5	Total Costs are cumulative over multiple years and FMS cases (SN-D-SAA; SN-D-SAC; SN-D-BAA; SN-D-QAT). Date of sale listed is the most current buy.
Japan	3/5/2015	149	32.8	Total Costs are cumulative over multiple years and FMS cases (JA-P-LTY; JA-P-LTD; JA-P-LTV; JA-P-LUD; JA-P-LVM; JA-P-LVY; JA-P-LUO; JA-P-LUP; JA-P-LVE; JA-P-LWC; JA-P-LWJ; JA-P-LWO; JA-P-LXB; JA-P-LXC; JA-P-LXD; JA-P-LXE; JA-P-LXF; JA-P-LXM; JA-P-LXN; JA-P-LXO; JA-P-LYC; JA-P-LYL; JA-P-LYQ; JA-P-LYP; JA-P-LYT; JA-P-LYV; JA-P-LYX; JA-P-LZG; JA-P-NAF). Date of sale listed is the most current buy.
Saudi Arabia	2/20/2015	241	18.6	Total Costs are cumulative over multiple years and FMS cases (SR-D-QAB; SR-D-SAI, SR-P-LCO; SR-D-QBP). Date of sale listed is the most current buy. *Not all cost data is available. 165 terminals without pricing.*
Belgium	1/20/2015	84	18.2	Total Costs are cumulative over multiple years and FMS cases (BE-D-DZV; BE-D-QAT, BE-P-LBB). Date of sale listed is the most current buy.
Canada	1/20/2015	144	31.3	Total Costs are cumulative over multiple years and FMS cases (CN-P-LHF; CN-P-LHS; CN-P-LIC; CN-

P-LIQ; CN-P-LJC, CN-P-LJR). Date of sale listed is the most current buy.

Poland	1/20/2015	78	16.6	Total Costs are cumulative over multiple years and FMS cases (PL-D-SAC; PL-P-LAM). Date of sale listed is the most current buy.
South Korea	12/29/2014	34	9.0	Total Costs are cumulative over multiple years and FMS cases (KS-P-BTV; KS-P-GOL; KS-P-LPN; KS-P-QDW; KS-P-BVB). Date of sale listed is the most current buy.
Finland	9/30/2014	120	23.2	Total Costs are cumulative over multiple years and FMS cases (FI-P-LBC; FI-P-LBD; FI-P-LBH; FI-P-LBJ). Date of sale listed is the most current buy.
New Zealand	9/30/2014	9	1.6	Date of sale listed is the most current buy on FMS case (NZ-P-LAJ; NZ-P-LAZ; NZ-P-LAU).
Chile	8/7/2014	25	3.7	Date of sale listed is the most current buy on FMS case CI-P-LCW.
Jordan	8/7/2014	34	5.6	Total Costs are cumulative over multiple years and FMS cases (JO-P-LAZ; JO-P-LBG; JO-D-QBK). Date of sale listed is the most current buy.
Portugal	8/7/2014	46	8.5	Date of sale listed is the most current buy on FMS case PT-D-NAE; PT-P-LDH.
Switzerland	8/5/2013	60	14.6	Date of sale listed is the most current buy on FMS case SZ-P-LAC; SZ-P-LAH.
United Arab Emirates	8/5/2013	19	3.3	Total Costs are cumulative over multiple years and FMS cases (AE-P-LAA; AE-B-UAF; AE-B-ZUG). Date of sale listed is the most current buy.
Taiwan	6/4/2013	196	59.4	Total Costs are cumulative over multiple years and FMS cases (TW-P-GNU; TW-B-YYV; TW-P-GMK; TW-P-LEJ; TW-P-SEG; TW-P-GMG). Date of sale listed is the most current buy.
Turkey	9/21/2012	314	61.1	Total Costs are cumulative over multiple years and FMS cases (TK-D-NCU; TK-P-LKT; TK-D-SMB). Date of sale listed is the most current buy.
Hungary	9/16/2010	22	4.1	Date of sale listed is the most current buy on FMS case HU-P-LAD.
Pakistan	9/16/2010	68	16.1	Total Costs are cumulative over multiple years and FMS cases (PK-D-NAP; PK-D-SAF). Date of sale listed is the most current buy.
Morocco	5/14/2010	30	4.8	Date of sale listed is the most current buy on FMS case MO-D-SAY.
Norway	6/23/2009	77	22.9	Total Costs are cumulative over multiple years and FMS cases (NO-D-OAF; NO-D-OAG; NO-P-LBE; NO-P-LBO). Date of sale listed is the most current buy.
Greece	12/22/2008	40	6.9	Total Costs are cumulative over multiple years and FMS cases (GR-B-XJU; GR-D-SNY). Date of sale listed is the most current buy.
Austria	5/12/2008	24	0.0	FMS total costs not releasable for Austria. AU-P-LAD.
Sweden	8/28/2006	28	4.9	Date of sale listed is the most current buy on FMS case SW-P-LAO.
Germany	2/20/2004	10	6.4	Date of sale listed is the most current buy on FMS

case GY-P-LGI.

Denmark	5/16/2002	3	0.9	Date of sale listed is the most current buy on FMS case DE-D-OAB.
---------	-----------	---	-----	---

Notes

The above FMS cases, with the exception of United Kingdom (UK-D-SAO; UK-P-LVE) and Australia (AT-P-SCI; AT-P-LFA) for MIDS Joint Tactical Radio System (MIDS JTRS) terminals, are for MIDS Low Volume Terminals (MIDS-LVT).

Direct Commercial Sales (DCS) totaling 968 MIDS-LVT terminals have been implemented to date with Australia (16), Belgium (2), Denmark (77), Greece (6), Iceland (3), Japan (2), Korea (183), North Atlantic Treaty Organization (NATO) Air Command and Control System (ACCS) Management Agency (NACMA) (72), Netherlands (149), NATO EuroFighter 2000 and Tornado Management Agency (36), Norway (31), Poland (2), Singapore (7), Sweden (140), Turkey (15) and United Kingdom (227). (Cost information for direct commercial sales is not available nor is date of sale). Per CJCSI 6510.0C, DCS sales for MIDS-LVT and MIDS JTRS are no longer sanctioned, except for a case-by-case basis with Australia, Canada, New Zealand, and the United Kingdom, or a one-time waiver has already been obtained.

Other foreign sales for 42 MIDS-LVT terminals at a cost of 12.2\$M were implemented through February 2015 with the European Participating Air Force (3) and German competitive buys (39).

Nuclear Costs

None


Unit Cost

Unit Cost Report

Item	BY 2003 \$M	BY 2003 \$M	% Change
	Current UCR Baseline (Nov 2013 APB)	Current Estimate (Dec 2015 SAR)	
Program Acquisition Unit Cost			
Cost	3031.0	3872.3	
Quantity	6233	8604	
Unit Cost	0.486	0.450	-7.41
Average Procurement Unit Cost			
Cost	1393.5	2133.5	
Quantity	5745	8000	
Unit Cost	0.243	0.267	+9.88

Item	BY 2003 \$M	BY 2003 \$M	% Change
	Original UCR Baseline (Mar 1994 APB)	Current Estimate (Dec 2015 SAR)	
Program Acquisition Unit Cost			
Cost	1091.4	3872.3	
Quantity	672	8604	
Unit Cost	1.624	0.450	-72.29
Average Procurement Unit Cost			
Cost	523.7	2133.5	
Quantity	630	8000	
Unit Cost	0.831	0.267	-67.87

Unit Cost History

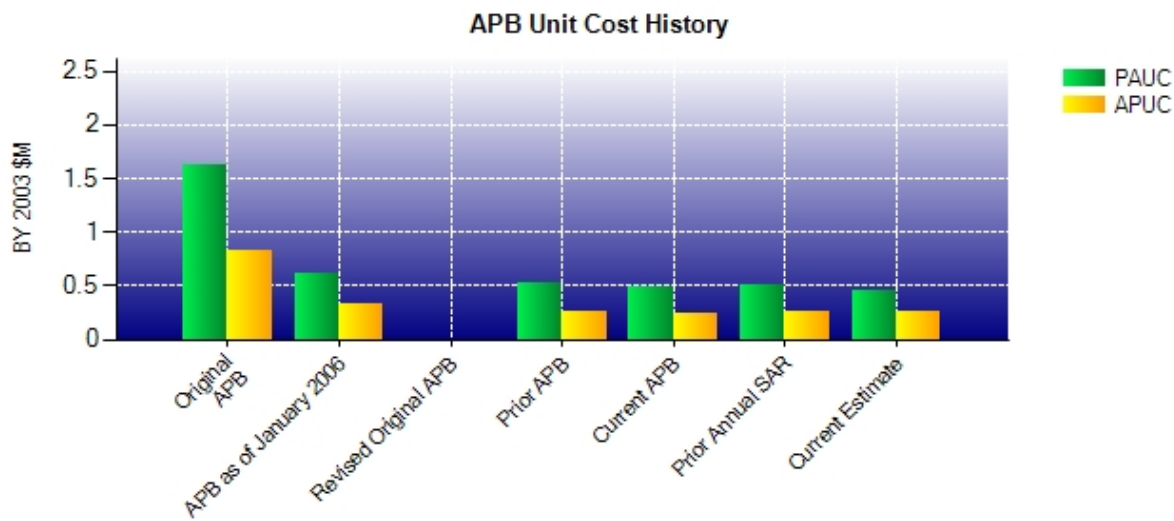

Item	Date	BY 2003 \$M		TY \$M	
		PAUC	APUC	PAUC	APUC
Original APB	Mar 1994	1.625	0.831	1.666	0.931
APB as of January 2006	Jun 2004	0.616	0.339	0.614	0.352
Revised Original APB	N/A	N/A	N/A	N/A	N/A
Prior APB	Apr 2012	0.533	0.255	0.573	0.280
Current APB	Nov 2013	0.486	0.243	0.535	0.276
Prior Annual SAR	Dec 2014	0.500	0.258	0.554	0.296
Current Estimate	Dec 2015	0.450	0.267	0.522	0.327

SAR Unit Cost History

Initial SAR Baseline to Current SAR Baseline (TY \$M)									
Initial PAUC Development Estimate	Changes								PAUC Production Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
1.670	-0.023	-1.090	0.015	-0.017	0.058	0.000	0.001	-1.056	0.614

Current SAR Baseline to Current Estimate (TY \$M)									
PAUC Production Estimate	Changes								PAUC Current Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
0.614	0.002	-0.159	-0.007	0.068	-0.003	0.000	0.007	-0.092	0.522

Initial SAR Baseline to Current SAR Baseline (TY \$M)									
Initial APUC Development Estimate	Changes								APUC Production Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
0.931	-0.019	-0.520	0.016	-0.036	-0.021	0.000	0.001	-0.579	0.352

Current SAR Baseline to Current Estimate (TY \$M)									
APUC Production Estimate	Changes								APUC Current Estimate
	Econ	Qty	Sch	Eng	Est	Oth	Spt	Total	
0.352	0.001	0.021	-0.007	-0.015	-0.032	0.000	0.007	-0.025	0.327

SAR Baseline History				
Item	SAR Planning Estimate	SAR Development Estimate	SAR Production Estimate	Current Estimate
Milestone I	N/A	N/A	N/A	N/A
Milestone II	N/A	Dec 1993	Dec 1993	Dec 1993
Milestone III	N/A	N/A	N/A	Dec 1999
IOC	N/A	Dec 2000	N/A	Jan 2001
Total Cost (TY \$M)	N/A	1119.5	1818.9	4492.7
Total Quantity	N/A	672	2964	8604
PAUC	N/A	1.666	0.614	0.522

The baseline includes separate Milestone (MS) III decisions for the MIDS Low Volume Terminal (MIDS-LVT) Variant (1) and MIDS-LVT Variant (3) and a separate IOC for each MIDS variant. A MS III decision was originally planned for the United States Army unique MIDS-LVT Variant (2) but it was replaced by an FRP decision approved by the Assistant Secretary of the Navy (Research, Development and Acquisition) in an ADM dated December 8, 2003.

Cost Variance

Summary TY \$M				
Item	RDT&E	Procurement	MILCON	Total
SAR Baseline (Production Estimate)	825.8	993.1	--	1818.9
Previous Changes				
Economic	+7.1	+14.5	--	+21.6
Quantity	+92.4	+1089.2	--	+1181.6
Schedule	-0.2	-31.5	--	-31.7
Engineering	+705.6	-69.2	--	+636.4
Estimating	+178.0	-319.0	--	-141.0
Other	--	--	--	--
Support	+3.7	+56.6	--	+60.3
Subtotal	+986.6	+740.6	--	+1727.2
Current Changes				
Economic	-1.6	-3.0	--	-4.6
Quantity	+13.9	+894.9	--	+908.8
Schedule	--	-26.0	--	-26.0
Engineering	--	-47.4	--	-47.4
Estimating	+52.3	+61.7	--	+114.0
Other	--	--	--	--
Support	--	+1.8	--	+1.8
Subtotal	+64.6	+882.0	--	+946.6
Total Changes	+1051.2	+1622.6	--	+2673.8
CE - Cost Variance	1877.0	2615.7	--	4492.7
CE - Cost & Funding	1877.0	2615.7	--	4492.7

Summary BY 2003 \$M				
Item	RDT&E	Procurement	MILCON	Total
SAR Baseline (Production Estimate)	869.4	955.4	--	1824.8
Previous Changes				
Economic	--	--	--	--
Quantity	+84.3	+850.4	--	+934.7
Schedule	-0.4	-9.0	--	-9.4
Engineering	+592.9	-53.9	--	+539.0
Estimating	+138.7	-278.6	--	-139.9
Other	--	--	--	--
Support	+3.2	+44.3	--	+47.5
Subtotal	+818.7	+553.2	--	+1371.9
Current Changes				
Economic	--	--	--	--
Quantity	+10.9	+636.0	--	+646.9
Schedule	--	-15.0	--	-15.0
Engineering	--	-33.4	--	-33.4
Estimating	+39.8	+35.8	--	+75.6
Other	--	--	--	--
Support	--	+1.5	--	+1.5
Subtotal	+50.7	+624.9	--	+675.6
Total Changes	+869.4	+1178.1	--	+2047.5
CE - Cost Variance	1738.8	2133.5	--	3872.3
CE - Cost & Funding	1738.8	2133.5	--	3872.3

Previous Estimate: December 2014

RDT&E	\$M	
Current Change Explanations	Base Year	Then Year
Revised escalation indices. (Economic)	N/A	-1.6
Quantity variance resulting from an increase of 35 MIDS Joint Tactical Radio System (JTRS) terminals (Air Force). (Quantity)	+8.4	+10.7
Quantity variance resulting from an increase of 11 MIDS-Low Volume Terminal (LVT) terminals and 6 MIDS JTRS terminals (Navy). (Quantity)	+2.5	+3.2
Revised estimate to align with FY 2017 PB to fully fund MIDS JTRS Tactical Targeting Network Technology (TTNT) (Navy). (Estimating)	+13.0	+18.5
Revised estimate for rate adjustments (Navy). (Estimating)	-1.7	-2.3
Congressional Reduction in FY 2017 (Navy). (Estimating)	-1.3	-1.8
Revised estimate for purchase of 4 MIDS-LVT Block Upgrade 2 retrofit kits for risk reduction terminals (Air Force). (Estimating)	+1.3	+1.6
FY 2014 - FY 2015 New funding for Investigation Reports for implementation of MIDS JTRS to Air Force Platforms (Air Force). (Estimating)	+8.5	+10.8
Additional Funding in FY 2015 for MIDS Modernization and MIDS JTRS TTNT (Navy). (Estimating)	+17.2	+21.9
Revised estimate for MIDS JTRS TTNT High Powered Amplifier technical development (Navy). (Estimating)	+2.0	+2.6
Adjustment for current and prior escalation. (Estimating)	+0.8	+1.0
RDT&E Subtotal	+50.7	+64.6

Procurement	\$M	
Current Change Explanations	Base Year	Then Year
Revised escalation indices. (Economic)	N/A	-3.0
Acceleration of procurement buy profile (Navy) F-18 earlier buy from FY 2015 to FY 2013 (Schedule)	0.0	-4.8
Quantity variance resulting from an increase of 65 MIDS-LVT terminals from 825 to 890 (Air Force). (Other Procurement, Air Force - OPAF) (Subtotal)	+13.0	+17.6
Quantity variance resulting from an increase of 65 MIDS-LVT terminals from 825 to 890 (Air Force). (OPAF) (Quantity)	(+19.2)	(+26.0)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-0.5)	(-0.6)
Allocation to Engineering resulting from Quantity change. (Engineering) (QR)	(-1.1)	(-1.6)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-4.6)	(-6.2)
Quantity variance resulting from an increase of 67 MIDS-LVT terminals and 1346 MIDS JTRS terminals (Air Force). (Aircraft Procurement, Air Force - APAF) (Subtotal)	+285.2	+399.5
Quantity variance resulting from an increase of 67 MIDS-LVT terminals and 1346 MIDS JTRS terminals (Air Force). (APAF) (Quantity)	(+417.8)	(+585.3)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-10.0)	(-14.1)
Allocation to Engineering resulting from Quantity change. (Engineering) (QR)	(-21.9)	(-30.8)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-100.7)	(-140.9)
Quantity variance resulting from an increase of 2 MIDS-LVT terminals from 425 to 427 (Army). (Other Procurement, Army - OPA) (Subtotal)	+0.4	+0.6
Quantity variance resulting from an increase of 2 MIDS-LVT terminals from 425 to 427 (Army). (OPA) (Quantity)	(+0.6)	(+0.8)

Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-0.2)	(-0.2)
Quantity variance resulting from an increase of 57 MIDS-LVT terminals and 107 MIDS JTRS terminals (Navy). (Other Procurement, Navy - OPN) (Subtotal)	+33.4	+44.6
Quantity variance resulting from an increase of 57 MIDS-LVT terminals and 107 MIDS JTRS terminals (Navy). (OPN) (Quantity)	(+48.2)	(+64.5)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-1.0)	(-1.3)
Allocation to Engineering resulting from Quantity change. (Engineering) (QR)	(-2.3)	(-3.1)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-11.5)	(-15.5)
Quantity variance resulting from an increase of 6 MIDS-LVT terminals and 26 MIDS JTRS terminals (Navy). (Shipbuilding and Conversion, Navy - SCN) (Subtotal)	+6.4	+11.0
Quantity variance resulting from an increase of 6 MIDS-LVT terminals and 26 MIDS JTRS terminals (Navy). (SCN) (Quantity)	(+9.5)	(+16.1)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-0.1)	(-0.2)
Allocation to Engineering resulting from Quantity change. (Engineering) (QR)	(-0.4)	(-0.8)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-2.6)	(-4.1)
Quantity variance resulting from an increase of 72 MIDS LVT terminals and 403 MIDS JTRS (Navy). (Aircraft Procurement, Navy - APN) (Subtotal)	+95.2	+136.8
Quantity variance resulting from an increase of 72 MIDS LVT terminals and 403 MIDS JTRS(Navy). (APN) (Quantity)	(+141.3)	(+203.0)
Allocation to Schedule resulting from Quantity change. (Schedule) (QR)	(-3.4)	(-5.0)
Allocation to Engineering resulting from Quantity change. (Engineering) (QR)	(-7.7)	(-11.1)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(-35.0)	(-50.1)
Quantity variance resulting from a decrease of 2 MIDS-LVT terminals from 60 to 58 (DoD). (Procurement Defense Agency - PDA) (Subtotal)	-0.4	-0.5
Quantity variance resulting from a decrease of 2 MIDS-LVT terminals from 60 to 58 (DoD). (PDA) (Quantity)	(-0.6)	(-0.8)
Allocation to Estimating resulting from Quantity change. (Estimating) (QR)	(+0.2)	(+0.3)
Revised estimation due to quantity change and retrofit inclusion (OPAF) (Estimating) (QR)	+14.6	+19.5
Revised estimation due to quantity change and retrofit inclusion (OPN) (Estimating) (QR)	+14.6	+20.9
Revised estimation due to quantity change and retrofit inclusion (APAF) (Estimating) (QR)	+18.8	+26.3
Revised estimation due to quantity change and retrofit inclusion (APN) (Estimating) (QR)	+134.9	+198.0
Revised estimation due to quantity change and retrofit inclusion (OPA). (Estimating) (QR)	+0.8	+2.2
Revised estimation due to quantity change and retrofit inclusion (SCN) (Estimating) (QR)	+6.0	+10.8
Adjustment for current and prior escalation. (Estimating)	+0.5	+0.7
Adjustment for current and prior escalation. (Support)	-0.2	-0.2
Decrease in other support for MIDS JTRS and MIDS-LVT due to change in estimation of support necessary for MIDS retrofit kits and repairs (Navy). (APN) (Support)	-1.8	-2.2
Increase in initial spares due to estimation change (Navy). (APN) (Support)	+1.6	+1.7
FY 2015 Increased support due to additional procurement of MIDS-LVT retrofit kits (Army). (OPA) (Support)	+0.7	+0.9
FY 2015 Increased quantity of spares resulting from additional procurement of MIDS-LVT spares (Army). (OPA) (Support)	+2.7	+3.5
FY 2015 Decrease in other support due to an estimating correction (Air Force)(APAF) (Support)	-1.5	-1.9
Procurement Subtotal	+624.9	+882.0

(QR) Quantity Related

Contracts

Contract Identification

Appropriation: Procurement
Contract Name: MIDS Production Contract
Contractor: BAE Systems/Rockwell Collins Data Link Solutions L.L.C. (DLS)
Contractor Location: 350 Collins Rd NE
 Cedar Rapids, IA 52498
Contract Number: N00039-10-D-0031
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: March 10, 2010
Definitization Date: March 10, 2010

Contract Price							
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
134.8	N/A	59	216.4	N/A	619	485.6	485.6

Target Price Change Explanation

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to exercising options on the IDIQ contract for award of more Delivery Orders (non-Earned Value (EV)).

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost variance and Schedule variance is not reported for this contract because the contract includes only the production portion, which is FFP and level of effort. The Delivery Orders with EVM are not reported in this Contract value.

Notes

The Production for MIDS-Low Volume Terminal (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS) terminals are on new contracts which have been added to the report.

The original value of the contract when awarded was \$134.8M in 2010. Since then more IDIQ orders have been awarded and options exercised increasing the value of the contract to \$485.6M (although only \$216.4M has been obligated).

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS-LVT terminals, MIDS JTRS terminals, and associated spares. FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and DLS. Current Contract Target Price reflects orders awarded to this vendor except for EV efforts which are accounted for separately.

This contract is more than 90% complete; therefore, this is the final report for this contract.

Contract Identification

Appropriation: Procurement
Contract Name: MIDS Production Contract
Contractor: ViaSat, INC
Contractor Location: 6155 El Camino Real
 Carlsbad, CA 92009
Contract Number: N00039-10-D-0032
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: March 10, 2010
Definitization Date: March 10, 2010

Contract Price							
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)	
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager
134.8	N/A	76	258.0	N/A	781	527.4	527.4

Target Price Change Explanation

The difference between the Initial Contract Price Target and the Current Contract Price Target is due to delivery orders not yet awarded.

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost variance and Schedule variance is not reported for this contract because the contract includes only the production portion, which is FFP and level of effort. The Delivery Orders with EVM are not reported in this Contract value.

Notes

The Production for MIDS-Low Volume Terminals (MIDS-LVT) and MIDS Joint Tactical Radio System (MIDS JTRS) terminals are on new contracts which have been added to the report.

The original value of the contract when awarded was \$134.8M in 2010. Since then more IDIQ orders have been awarded and options exercised increasing the value of the contract to \$527.4M (although only \$258M has been obligated).

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS-LVT terminals, MIDS JTRS terminals, and associated spares. FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and Data Link Solutions L.L.C.. Current Contract Target Price reflects orders awarded to this vendor except for Earned Value efforts which are accounted for separately.

This contract is more than 90% complete; therefore, this is the final report for this contract.

Contract Identification

Appropriation: Procurement
Contract Name: MIDS JTRS Production Contract
Contractor: BAE Systems/Rockwell Collins Data Link Solutions L.L.C. (DLS)
Contractor Location: 350 Collins Rd NE
 Cedar Rapids, IA 52498
Contract Number: N00039-15-D-0007
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: June 17, 2015
Definitization Date: June 17, 2015

Contract Price								
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)		
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager	
50.1	N/A	153	50.1	N/A	153	478.6	478.6	

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost and Schedule variance is not reported for this contract, because thus far no delivery order requiring EVM has been awarded.

Notes

This is the first time this contract is being reported.

The overall value with all Options included of this contract is \$478.6M. In the future, more IDIQ orders will be awarded and options exercised increasing the current of the contract.

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS Joint Tactical Radio terminals. FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and DLS. Current Contract Target Price reflects orders awarded to this vendor.

Contract Identification

Appropriation: Procurement
Contract Name: MIDS Production Contract
Contractor: ViaSat, INC
Contractor Location: 6155 El Camino Real
 Carlsbad, CA 92009
Contract Number: N00039-15-D-0008
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: May 28, 2015
Definitization Date: May 28, 2015

Contract Price								
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)		
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager	
19.6	N/A	42	19.6	N/A	42	478.6	478.6	

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost and Schedule variance is not reported for this contract, because thus far no delivery order requiring EVM has been awarded.

Notes

This is the first time this contract is being reported.

The overall value with all Options included of this contract is \$478.6M. In the future, more IDIQ orders will be awarded and options exercised increasing the current of the contract.

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS Joint Tactical Radio System terminal. FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and DLS. Current Contract Target Price reflects orders awarded to this vendor.

Contract Identification

Appropriation: Procurement
Contract Name: MIDS-LVT Production Contract
Contractor: BAE Systems/Rockwell Collins Data Link Solutions L.L.C. (DLS)
Contractor Location: 350 Collins Rd NE
 Cedar Rapids, IA 52498
Contract Number: N00039-15-D-0042
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: August 27, 2015
Definitization Date: August 27, 2015

Contract Price								
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)		
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager	
14.6	N/A	57	14.6	N/A	57	538.5	538.5	

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost and Schedule variance is not reported for this contract, because thus far no delivery order requiring EVM has been awarded.

Notes

This is the first time this contract is being reported.

The overall value with all Options included of this contract is \$538.5M. In the future, more IDIQ orders will be awarded and options exercised increasing the current of the contract.

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS-Low Volume Terminal (MIDS-LVT). FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and DLS. Current Contract Target Price reflects orders awarded to this vendor.

Contract Identification

Appropriation: Procurement
Contract Name: MIDS Production Contract
Contractor: ViaSat, INC
Contractor Location: 6155 El Camino Real
 Carlsbad, CA 92009
Contract Number: N00039-15-D-0043
Contract Type: Indefinite Delivery Indefinite Quantity (IDIQ), Firm Fixed Price (FFP), Cost Plus Fixed Fee (CPFF)
Award Date: August 21, 2015
Definitization Date: August 21, 2015

Contract Price								
Initial Contract Price (\$M)			Current Contract Price (\$M)			Estimated Price At Completion (\$M)		
Target	Ceiling	Qty	Target	Ceiling	Qty	Contractor	Program Manager	
5.1	N/A	26	5.1	N/A	26	514.3	514.3	

Cost and Schedule Variance Explanations

Cost and Schedule Variance reporting is not required on this (IDIQ/FFP/CPFF) contract.

General Contract Variance Explanation

Cost and Schedule variance is not reported for this contract, because thus far no delivery order requiring EVM has been awarded.

Notes

This is the first time this contract is being reported.

The overall value with all Options included of this contract is \$514.3M. In the future, more IDIQ orders will be awarded and options exercised increasing the current of the contract.

This production contract includes nonrecurring engineering, supportability, and the manufacture of MIDS-Low Volume Terminal (MIDS-LVT). FMS are not included in the supplemental contract cost information.

This is a Multiple Award Firm Fixed Price IDIQ contract. Delivery Orders are competed between two vendors, ViaSat and DLS. Current Contract Target Price reflects orders awarded to this vendor.

Deliveries and Expenditures

Deliveries				
Delivered to Date	Planned to Date	Actual to Date	Total Quantity	Percent Delivered
Development	520	520	604	86.09%
Production	4420	4440	8000	55.50%
Total Program Quantity Delivered	4940	4960	8604	57.65%

Expended and Appropriated (TY \$M)			
Total Acquisition Cost	4492.7	Years Appropriated	27
Expended to Date	3090.3	Percent Years Appropriated	77.14%
Percent Expended	68.78%	Appropriated to Date	3248.8
Total Funding Years	35	Percent Appropriated	72.31%

The above data is current as of February 09, 2016.

Total deliveries listed above do not contain EuroMIDS (non-U.S. vendor) terminals (which are not reported in the SAR).

Operating and Support Cost

Cost Estimate Details

Date of Estimate:	February 26, 2016
Source of Estimate:	POE
Quantity to Sustain:	8000
Unit of Measure:	Terminal
Service Life per Unit:	20.00 Years
Fiscal Years in Service:	FY 1996 - FY 2044

The O&S costs are based on the POE (dated February 26, 2016), which was evaluated by the Air Force Cost Analysis Agency and Naval Center for Cost Analysis in support of the MIDS Joint Tactical Radio System (MIDS JTRS) Full Production & Fielding (FP&F) decision. The quantity of 8,000 includes U.S. only terminals currently fielded and on contract plus known requirements for FY 2015 through FY 2044. This period includes a phase-in, steady state, and phase-down profile. Development units have no sustainment costs.

The current production terminal procurement estimate increased by a total of 2,149 terminals due to the procurement order from the U.S. Air Force (Platforms: F-15, F-16, F-22).

Sustainment Strategy

The annual operating hours per aircraft for peacetime deployment are estimated to be approximately 400. The annual operating hours per ship for peacetime deployment are estimated to be 3,977. The annual operating hours per Army Ground Air Defense station are estimated to be 2,212.

For Navy aircraft and Army platforms, maintenance is a three-level structure (i.e. Organizational, Intermediate/Direct Support and Depot). For Navy ships and Air Force aircraft platforms it is a two-level structure (i.e. Organizational and Depot). Navy aircraft support costs assume the use of the Consolidated Automated Support System at the Intermediate level of maintenance. The terminal reliability and maintainability characteristics used are consistent with the requirements contained in the ORD.

Antecedent Information

No Antecedent. The MIDS Low Volume Terminal (MIDS-LVT) does not replace an existing DoD system because it provides Link 16 capability to platforms that were unable to employ analogous systems due to space and weight constraints. The MIDS JTRS terminal is a form, fit, and function replacement and upgrade for MIDS-LVT in selected DoD systems.

Annual O&S Costs BY2003 \$K		
Cost Element	MIDS Average Annual Cost Per Terminal	N/A (Antecedent)
Unit-Level Manpower	0.250	--
Unit Operations	0.000	--
Maintenance	0.440	--
Sustaining Support	4.120	--
Continuing System Improvements	5.430	--
Indirect Support	0.000	--
Other	0.000	--
Total	10.240	--

Item	Total O&S Cost \$M			N/A (Antecedent)
	MIDS		N/A (Antecedent)	
	Current Production APB Objective/Threshold	Current Estimate		
Base Year	1176.6	1294.3	1638.4¹	N/A
Then Year	1573.7	N/A	2184.5	N/A

¹ APB O&S Cost Breach

Equation to Translate Annual Cost to Total Cost

The calculation of total O&S costs is based on total quantities of 8000 multiplied by an economic life of 20 years multiplied by a unit cost of \$10.24K per year.

O&S Cost Variance		
Category	BY 2003 \$M	Change Explanations
Prior SAR Total O&S Estimates - Dec 2014 SAR	1198.3	
Programmatic/Planning Factors	440.1	Increased quantity
Cost Estimating Methodology	0.0	
Cost Data Update	0.0	
Labor Rate	0.0	
Energy Rate	0.0	
Technical Input	0.0	
Other	0.0	
Total Changes	440.1	
Current Estimate	1638.4	

Disposal Estimate Details

Date of Estimate:

Source of Estimate:

Disposal/Demilitarization Total Cost (BY 2003 \$M):

Disposal costs are not identified at this time.
