

Space and Missile Systems Center



Military GPS User Equipment (MGUE)

Lt Col James "Mutt" Wilson
Program Manager
29 Apr 15

Information contained in this briefing cannot be construed as contractual direction

Report Documentation Page

Form Approved
OMB No. 0704-0188

Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.

1. REPORT DATE 29 APR 2015		2. REPORT TYPE		3. DATES COVERED 00-00-2015 to 00-00-2015	
4. TITLE AND SUBTITLE Military GPS User Equipment (MGUE)				5a. CONTRACT NUMBER	
				5b. GRANT NUMBER	
				5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)				5d. PROJECT NUMBER	
				5e. TASK NUMBER	
				5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Air Force Space Command, Space and Missile Systems Center, Los Angeles AFB, El Segundo, CA, 90245				8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)	
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited					
13. SUPPLEMENTARY NOTES Presented at the GPS Partnership Council 2015 (GPSPC15), held April 29 to May 1, 2015, at the Los Angeles AFB, CA.					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT Same as Report (SAR)	18. NUMBER OF PAGES 13	19a. NAME OF RESPONSIBLE PERSON
a REPORT unclassified	b ABSTRACT unclassified	c THIS PAGE unclassified			



Overview

SPACE AND MISSILE SYSTEMS CENTER

- MGUE Acquisition Strategy
- MGUE Increment 1 (Inc 1) Schedule
- MGUE Inc 1 Test Plan
- MGUE Increment 2 (Inc 2) Plan
- M-Code Receiver Statistics



MGUE Program Summary

SPACE AND MISSILE SYSTEMS CENTER


- Incremental Acquisition effort to develop form factors
 - Increment 1 (Inc 1): Ground (GB-GRAM-M) and Aviation/Maritime (GRAM-S/M)
 - Inc 1 form factors evaluated to be at high level of maturity
- Responded to Acquisition Decision Memorandum 20 Feb 14
 - Direction from USD(AT&L) to accelerate MGUE Increment 1
 - Pulled forward items from EMD phase and proceeding to MS B/C
 - Updated Acquisition Strategy Document, signed 10 Apr 15
- Requirements approved by JROC on 24 Jul 14
- Integrate Inc 1 form factors into service-nominated lead platforms
 - Ground: DAGR Distributed Device (D3) and Joint Light Tactical Vehicle (JLTV)
 - Air: B-2
 - Maritime: Arleigh Burke Class Missile Destroyer

MGUE Inc 1 Is On An Accelerated Path

MGUE Inc 1 Content

SPACE AND MISSILE SYSTEMS CENTER

- A commercial market driven acquisition approach
- Accelerating from TD phase to production

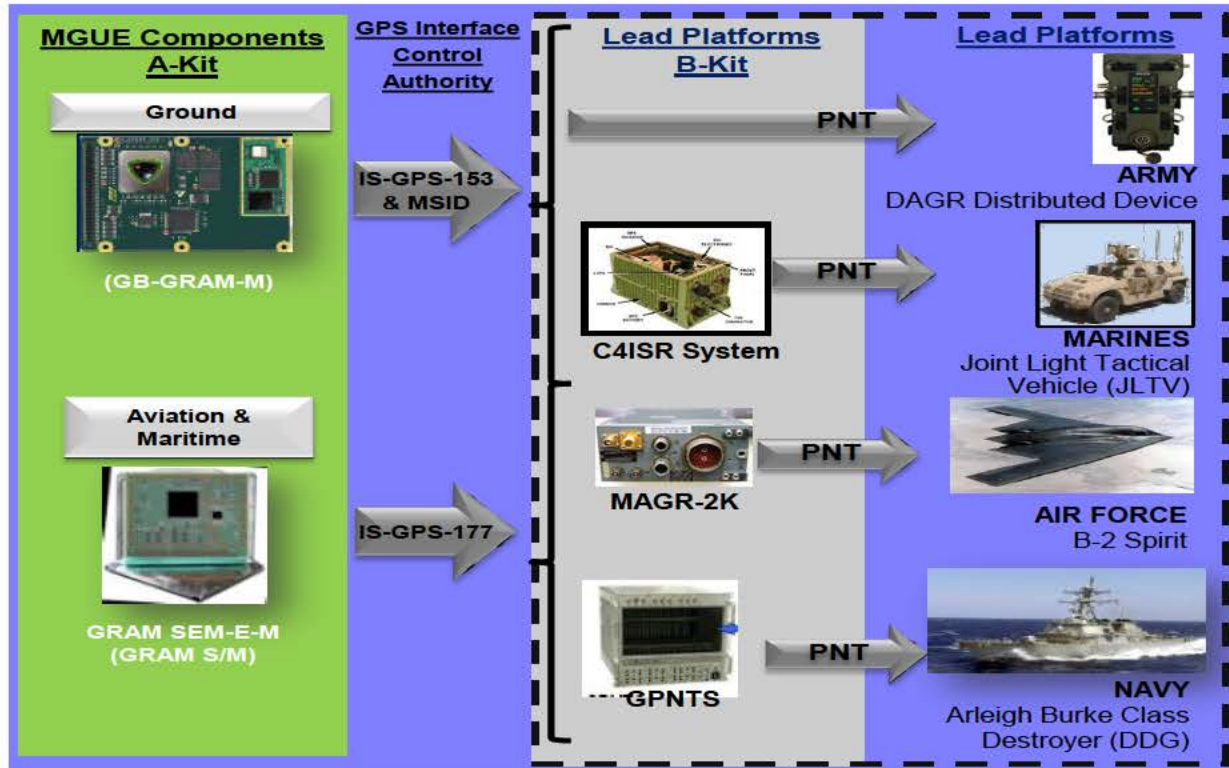


Incremental acquisition strategy sets basis for future




MGUE Inc 1 Program Schedule

SPACE AND MISSILE SYSTEMS CENTER

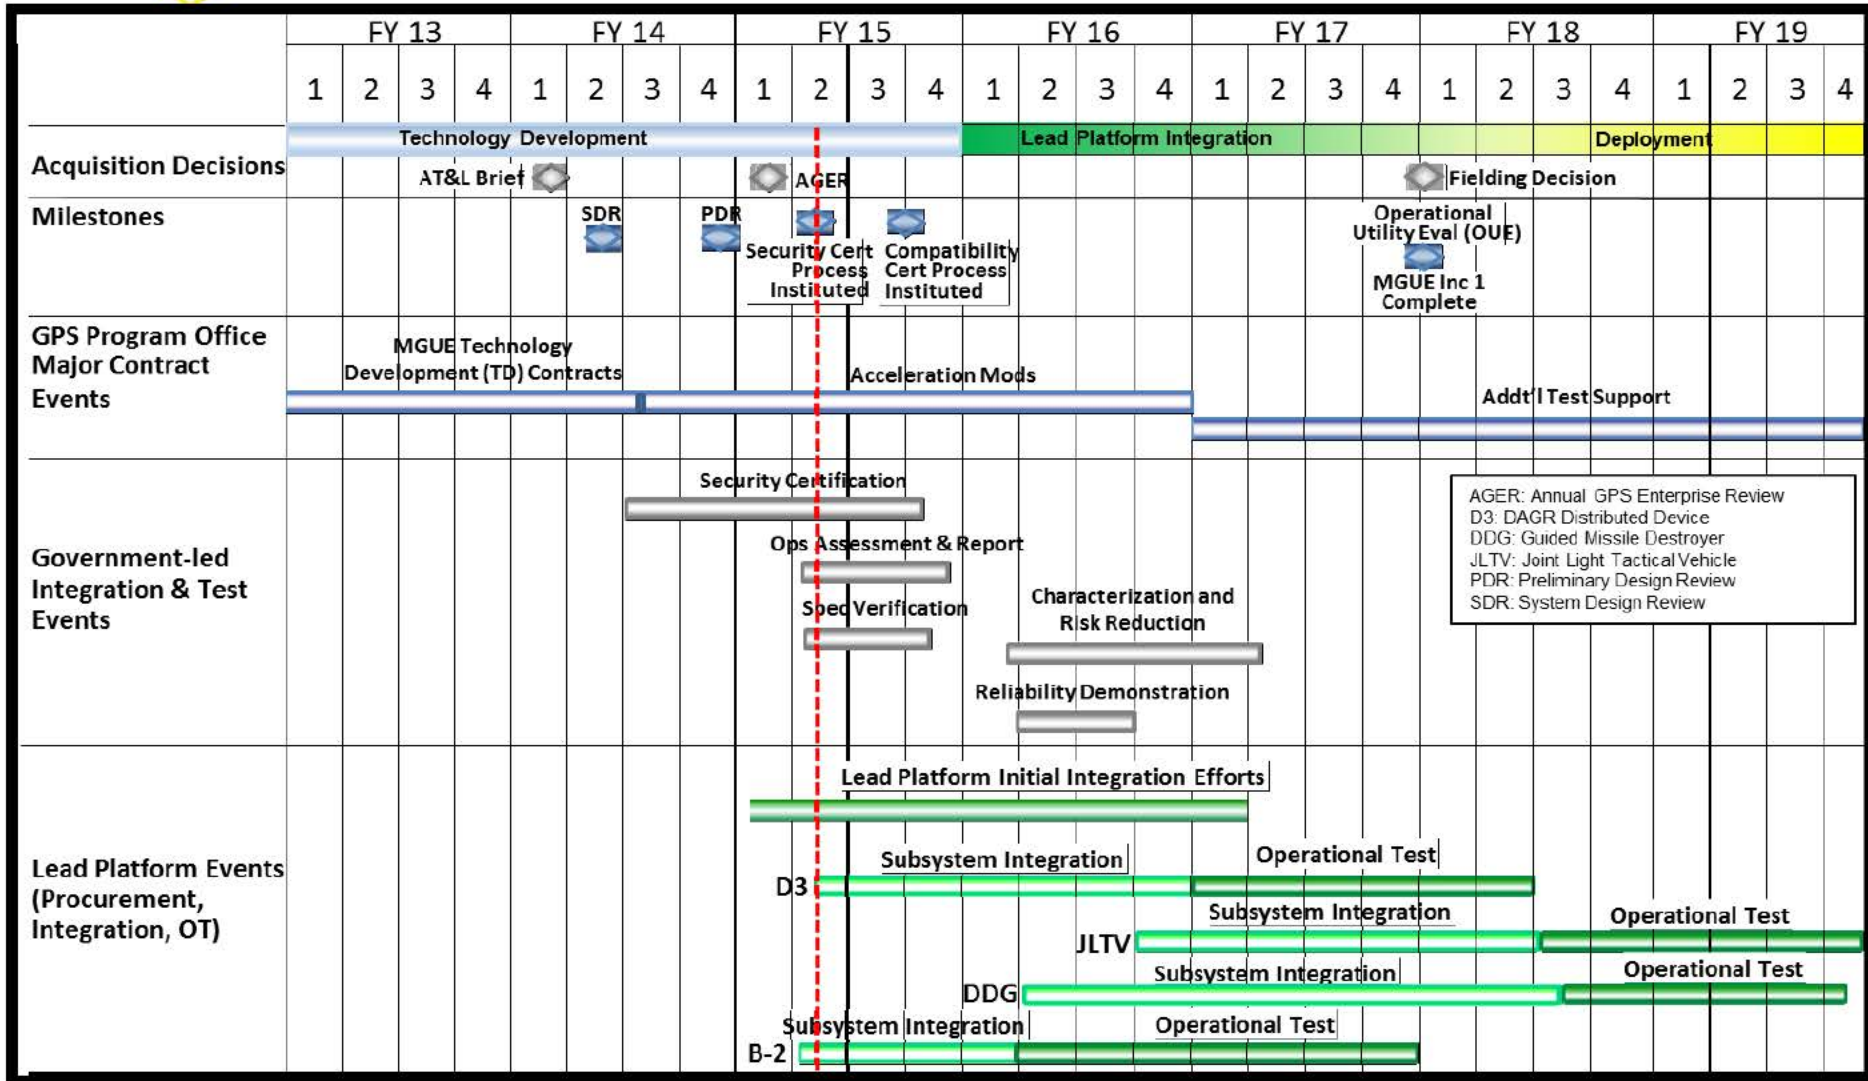

MGUE Test Strategy: Path to Operational Test in FY16

SPACE AND MISSILE SYSTEMS CENTER

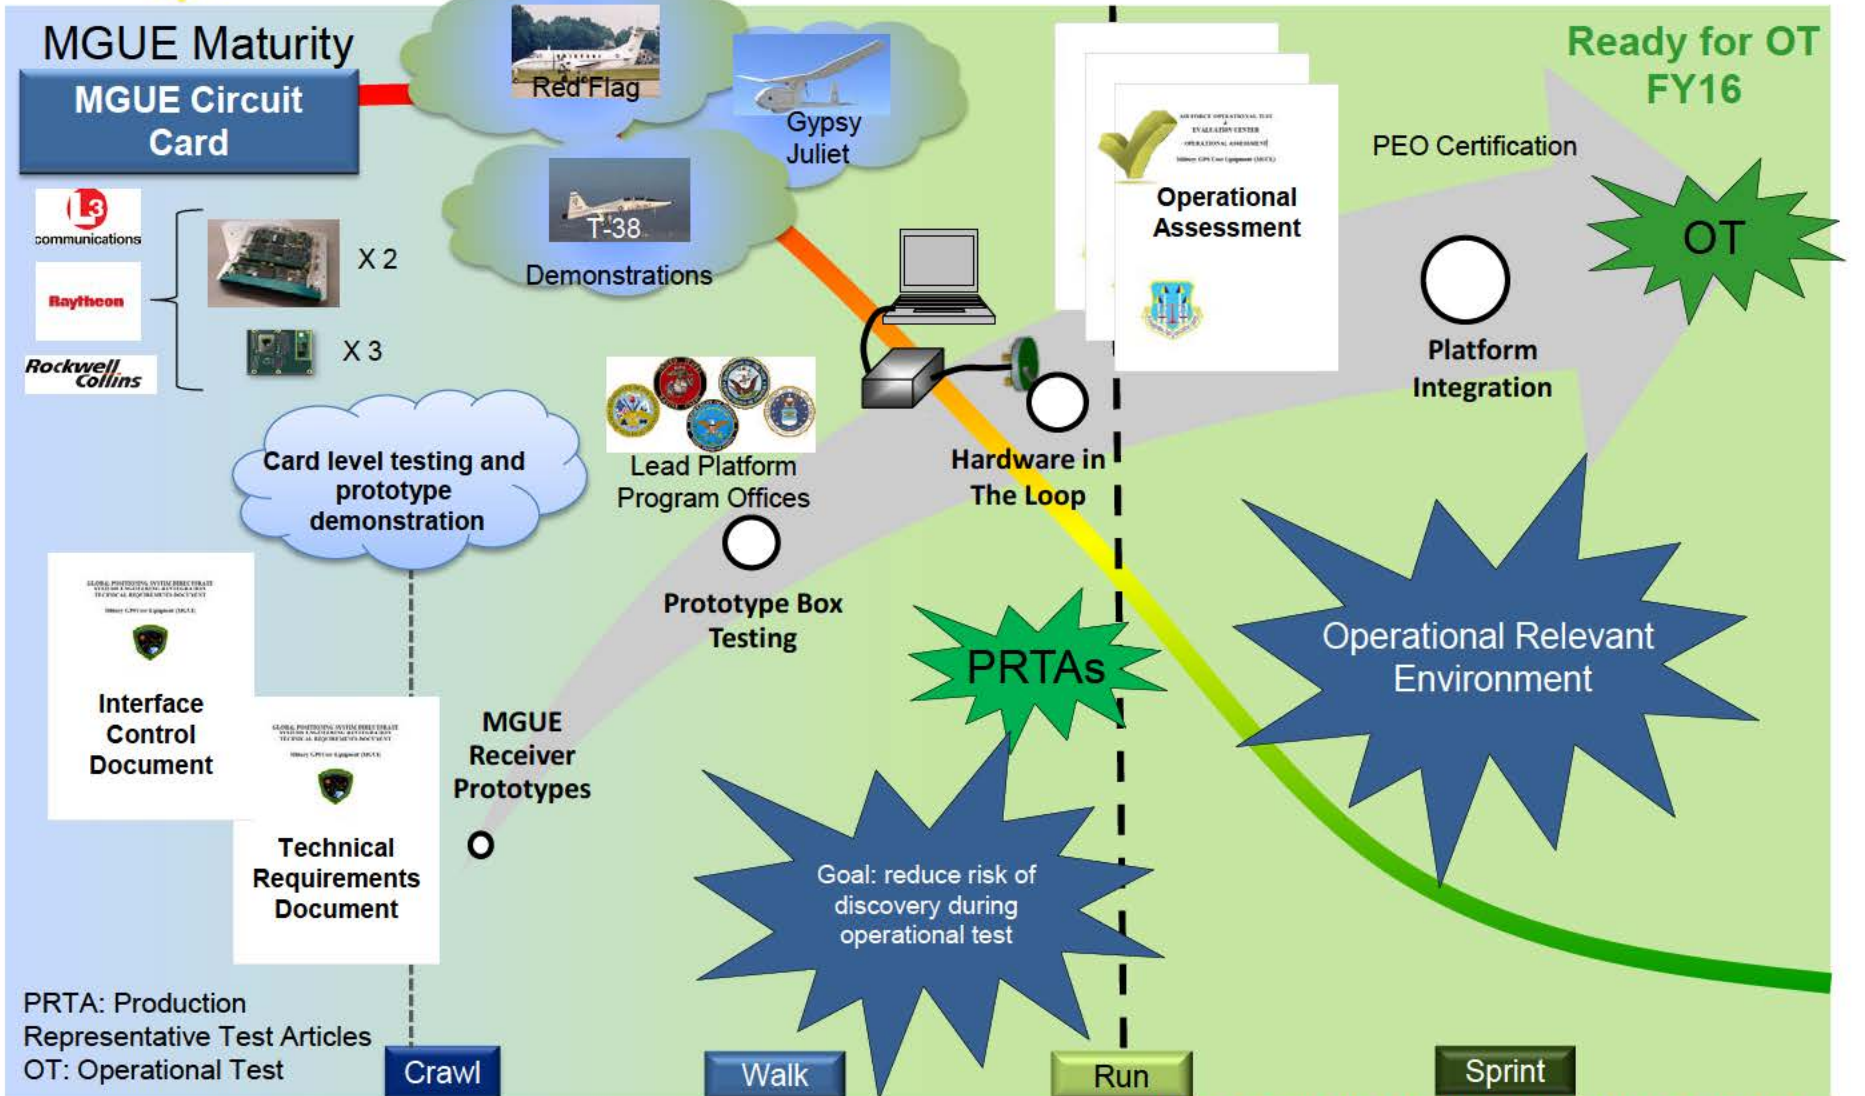

MGUE Performance: NavFest 2015

SPACE AND MISSILE SYSTEMS CENTER

- Utilized C-12J to showcase MGUE capabilities
 - More mature hardware/software than Red Flag
 - Additional early integration of B-2 receiver
 - Able to track M-Code in jamming environment
- Test Successful – MGUE card held lock!
 - M-Code tracked in both contested & benign environments



Aviation Receiver Held M-Code, All Other GPS Receivers Lost Lock



MGUE Inc 2 Current Status

SPACE AND MISSILE SYSTEMS CENTER

- JCIDS: Inc 2 Capabilities Development Document (CDD) in coordination
 - AFROC approved Draft CDD
 - Defines 3 items:
 - Precision Guided Munitions (PGM)
 - Space Receiver
 - Handheld (HH)

- PPBE: FY16 PB adds MGUE Inc 2
 - Starts in FY17, accelerating two years from FY19 start



Inc 2 Acceleration: Ongoing Efforts to Leverage Inc 1

SPACE AND MISSILE SYSTEMS CENTER

- Possible Materiel solutions exists for 2 of 3 Inc 2 Platforms
 - Teaming with Army to integrate Increment 1 (Inc 1) technology into Precision Guided Munitions (PGM)
 - Analysis indicates Inc 1 technology can withstand PG environments
 - AF developing low size/weight/power GPS M-Code space receiver
 - Completed Preliminary Design Reviews – Mar 2015
- Potential materiel solution for third platform
 - Investigating NDI to meet Handheld requirements



MGUE Inc 2: Handheld Acceleration

SPACE AND MISSILE SYSTEMS CENTER

- Continue accelerated commercial market driven approach by using existing Handheld with MGUE Inc 1 receiver
- Inc 2 requires handheld as an end item
- Opportunity to leverage Inc 1 efforts to handheld application
- USAF conducting market research of handheld vendors with potential to integrate MGUE Inc 1 ASIC into an existing product
- Seeking approval to pursue handheld as a non-developmental item



History of GPS User Equipment Development at SMC

SPACE AND MISSILE SYSTEMS CENTER



Small Lightweight GPS Receiver (SLGR)



Precision Lightweight GPS Receiver (PLGR)



180,000 units, Bosnia and OIF

Defense Advanced GPS Receiver (DAGR)



500,000 units, since 2005

Ground Based-GPS Receiver Application Module (GB-GRAM)



100,000 units, since 2005

MGUE Next Step in Long History




User Equipment Fielding vs Availability

SPACE AND MISSILE SYSTEMS CENTER



User Equipment	Quantity in the field
DAGR (SAASM)	500,000+
GB-GRAM (SAASM)	100,000+
Projected M-Code Receivers (FY17-FY30)	~1.5M+

SAASM Receivers Processed

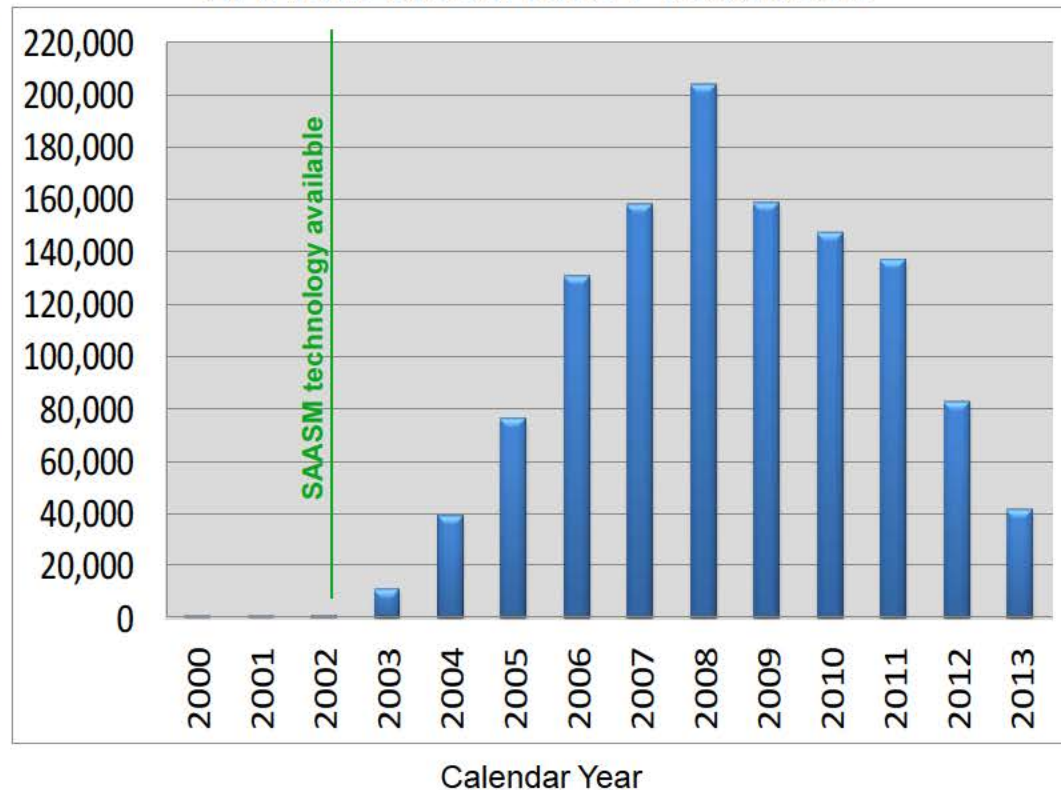

DAGR: Defense Advanced GPS Receiver
 GB-GRAM: Ground-Based GPS Receiver Application Module
 SAASM: Selective Availability Anti-Spoofing Module

M-Code receiver demand expected to increase with availability



Summary

SPACE AND MISSILE SYSTEMS CENTER

- MGUE is an incremental acquisition approach
- MGUE is operating on time
- MGUE Inc 1 accelerating to production
- MGUE Increment 2 will be a pre-planned product improvement
- M-Code is the way forward for GPS receivers
