

712CD

75TH MORSS CD Cover Page

If you would like your presentation included in the 75th MORSS Final Report CD it must :

1. *Be unclassified, approved for public release, distribution unlimited, and is exempt from U.S. export licensing and other export approvals including the International Traffic in Arms Regulations (22CFR120 et seq.);*
2. Include MORS Form 712CD as the first page of the presentation;
3. Have an approved MORS form 712 A/B and
4. Be turned into the MORS office no later than: **DEADLINE: 14 June 2007 (Late submissions will not be included.)**

Author Request (To be completed by applicant) - The following author(s) request authority to disclose the following presentation in the MORSS Final Report, for inclusion on the MORSS CD and/or posting on the MORS web site.

Name of Principal Author and all other author(s):

Kurt Willstatter, Richard "Andy" Campbell, and Kirk L. Hoy

Principal Author's Organization and address:

Summit Engineering Group
102 Paul Mellon Court, Suite 1
Waldorf, MD 20602

Phone: (301) 645-3535

Fax: (301) 645-3950

Email: kwillstatter@summit-group.com

Please use the same title listed on the 75th MORSS Disclosure Form 712 A/B. If the title of the presentation has changed please list both.)

Original title on 712 A/B:

Modeling the Life Cycle Cost of Protecting US Commercial Aircraft

If the title was revised please list the original title above and the revised title here:

PRESENTED IN:

WORKING GROUP: 4, 19, 27, 30

DEMONSTRATION:

COMPOSITE GROUP:

POSTER:

SPECIAL SESSION 1:

TUTORIAL:

SPECIAL SESSION 2:

OTHER:

SPECIAL SESSION 3:

This presentation is believed to be: *Unclassified, approved for public release, distribution unlimited, and is exempt from U.S. export licensing and other export approvals including the International Traffic in Arms Regulations (22CFR120 et seq.)*


Report Documentation Page

Form Approved
OMB No. 0704-0188

Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.

1. REPORT DATE 01 JUN 2007	2. REPORT TYPE N/A	3. DATES COVERED -	
4. TITLE AND SUBTITLE Modeling The Life Cycle Cost Of Protecting Us Commercial Aircraft		5a. CONTRACT NUMBER	
		5b. GRANT NUMBER	
		5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)		5d. PROJECT NUMBER	
		5e. TASK NUMBER	
		5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Summit Engineering Group Waldorf, MD 20602		8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)		10. SPONSOR/MONITOR'S ACRONYM(S)	
		11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release, distribution unlimited			
13. SUPPLEMENTARY NOTES See also ADM202526. Military Operations Research Society Symposium (75th) Held in Annapolis, Maryland on June 12-14, 2007., The original document contains color images.			
14. ABSTRACT			
15. SUBJECT TERMS			
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified	UU
			18. NUMBER OF PAGES 22
			19a. NAME OF RESPONSIBLE PERSON

Modeling the Life Cycle Cost of Protecting US Commercial Aircraft

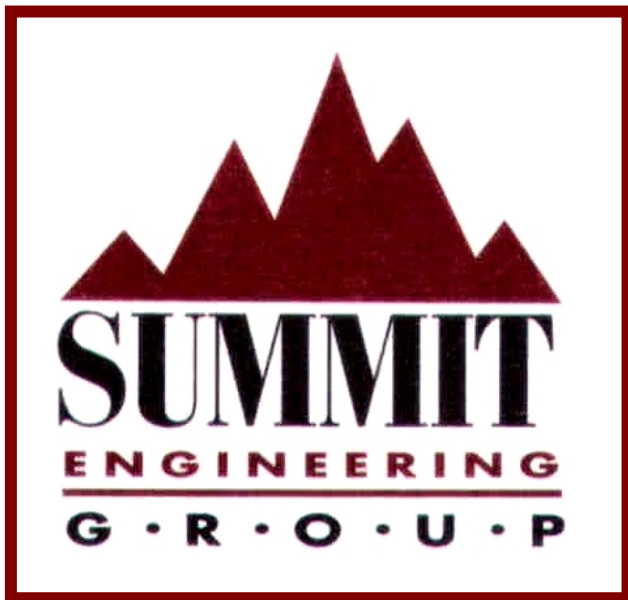

Presentation to:
75th MORS Symposium
Annapolis, MD
12-14 June 2007

By: **Mr. Kurt Willstatter**
Mr. Richard “Andy” Campbell
Summit Engineering Group
102 Paul Mellon Court, Suite 1
Waldorf, Maryland 20602
301-645-3535 (-3950 fax)

Kwillstatter@summit-group.com

Acampbell@summit-group.com

www.summit-group.com

Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Preface

- This briefing focuses on the Life Cycle Cost (LCC) estimate developed by Summit Engineering Group for the Counter-MANPADS (CM) Program managed by the Department of Homeland Security (DHS)
- The completeness and accuracy of the LCC estimate was a key requirement

The Risk of Any Specific Threat is NOT Addressed Here



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Acronyms

- A/C = Aircraft
- CM = Counter-MANPADS & Countermeasures
- DHS = Department of Homeland Security
- DIRCM = Directed Infrared Countermeasures
- DT&E = Developmental Test and Evaluation
- ECP = Engineering Change Proposal
- LCC = Life Cycle Cost
- LOE = Level of Effort
- LRU = Line Replicable Unit
- MFHBF = Mean Flight Hours Between Failure
- NB = Narrow Body
- O&S = Operations and Support
- OEM = Original Equipment Manufacturer
- OGC = Other Government Costs
- OT&E = Operational Test and Evaluation
- P³I = Pre-Planned Product Improvement
- PM = Program Management
- PMP = Prime Mission Product
- RDT&E = Research, Development, Test, and Evaluation
- SE = System Engineering
- ST&E = System Test and Evaluation
- STC = Supplemental Type Certificate
- T₁ = First Unit
- WB = Wide Body



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Discussion Topics

- Background
- LCC Estimate
 - Goals
 - Risks
 - Risk Mitigation
- Key Assumptions
- LCC Estimate
 - Summary
 - RDT&E Phase
 - Production & Deployment Phase
 - Operations & Support (O&S) Phase
 - De-Modification & Disposal Phase
- Risk Insights
- Related Activities
- Questions



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Background

- DHS Science and Technology (S&T) Directorate tasked with demonstrating the technical feasibility, assessing life cycle costs, and evaluating the effectiveness of protecting commercial aircraft against the threat of Man-Portable Air Defense Systems (MANPADS)
- Primarily focused on mature Directed Infrared Countermeasure (DIRCM) systems
 - Self-contained pod
 - Distributed installation
- Complex problem due to
 - Multitude of aircraft types (Wide-body vs. Narrow-body)
 - Varying flight profiles as a function of aircraft type
 - Multiple operating environments (Cargo vs. Passenger)
 - Potentially large lost revenue costs for installations that fall outside normal maintenance cycles

Aircraft Demographics

- Wide body (WB)
 - Multi-aisle
 - Longer flights at altitude
 - More passengers per aircraft
- Narrow body (NB)
 - Single-aisle
 - Shorter, more frequent flights
 - Fewer passengers per aircraft, but higher total passenger volume
- Cargo is ~1,000 of total

Aircraft	Type	Fleet Size*
777	WB	122
767	WB	334
747	WB	108
DC/MD10	WB	99
MD11	WB	74
A300	WB	140
A310	WB	64
A330	WB	29
A318/19	NB	279
A320/21	NB	368
717/727	NB	271
737	NB	1241
757	NB	617
DC8,9/MD80/90	NB	703
	Total**	4,449

* Circa 2005 ** Excludes ~1,600 regional jets




Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

LCC Estimate Goals

- Comprehensive accounting of all foreseeable costs
- Explicitly address key LCC parameters
 - STCs and follow-on P3I/testing
 - Production rate tooling/test equipment (& for depot)
 - Investments to achieve reliability growth
 - CM system weight/drag impacts to fuel consumption
- Consistent approaches among vendors' LCC estimates so individual results could be leveraged
- Exercise LCC across various quantity profiles

The goal was an independent, vendor-neutral Cost Estimate at about the 70% confidence level

Civil Counter-MANPADS Cost Elements

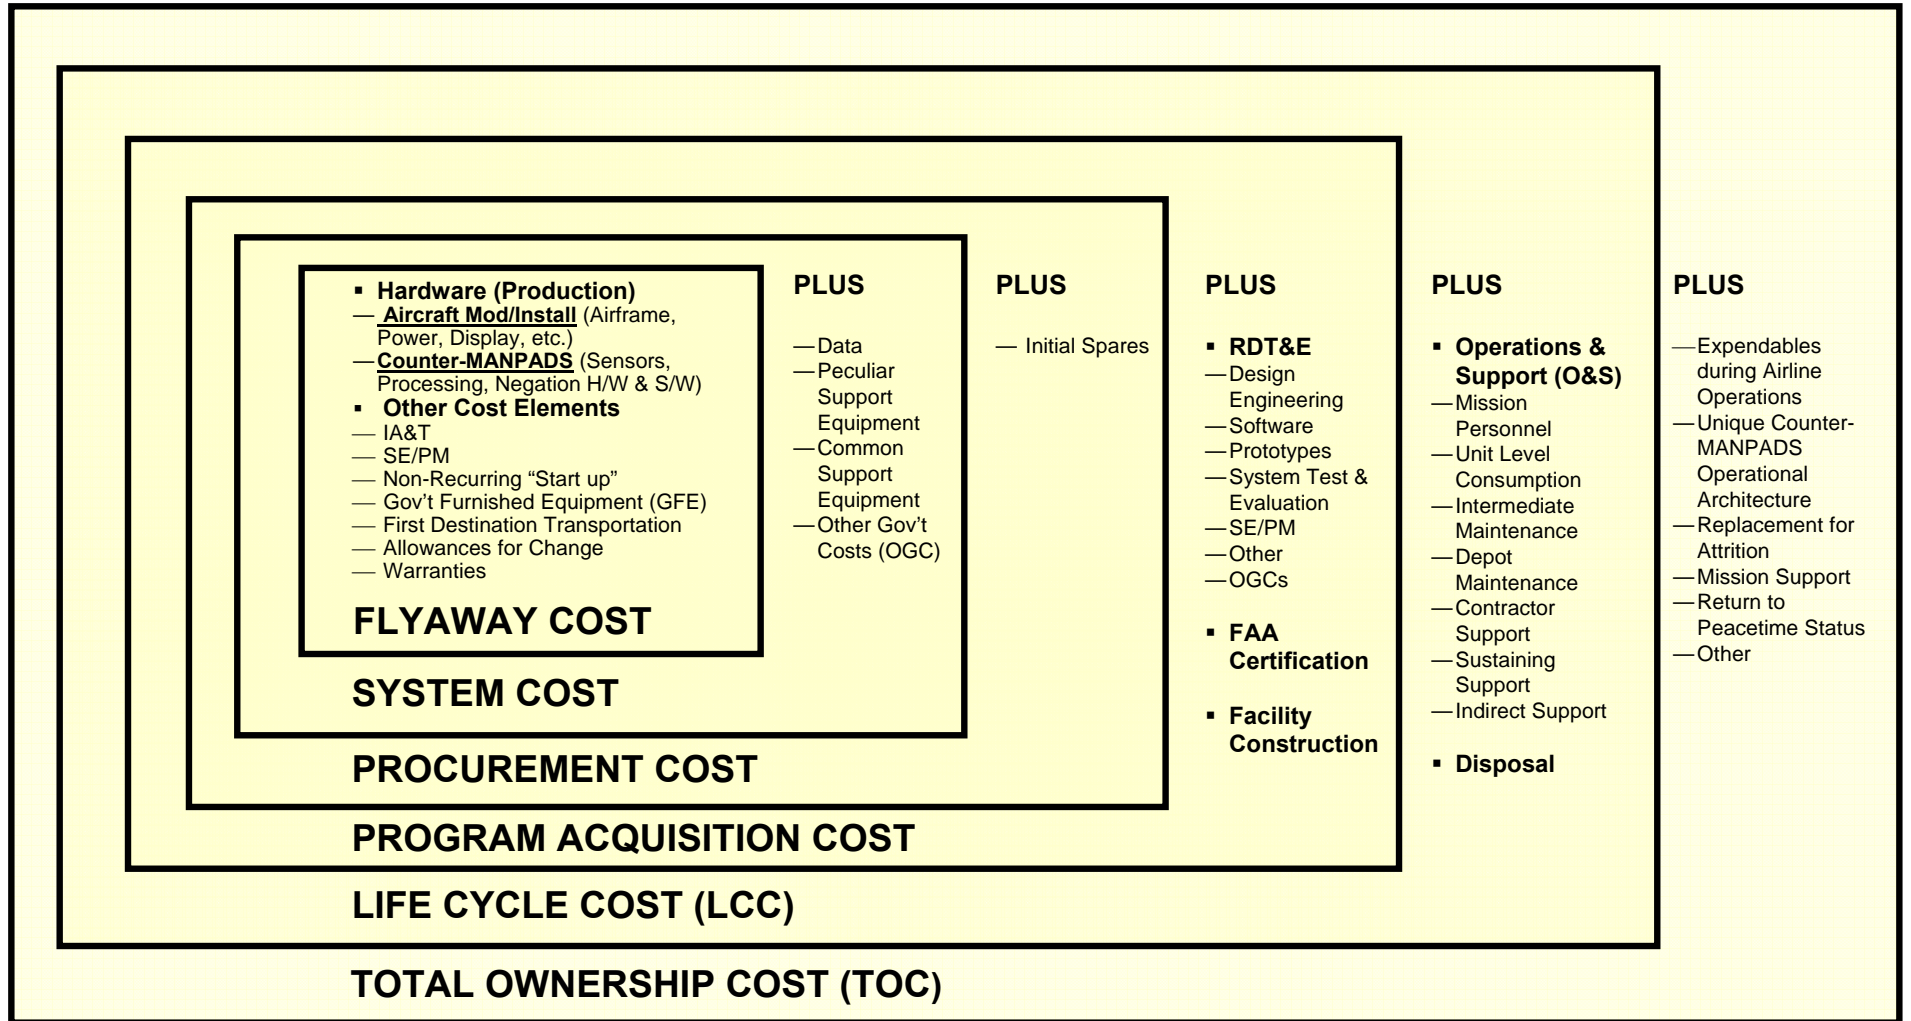

Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

LCC Estimate Risks

- Inaccurate assumptions
- Vendor optimism
 - Initial system reliability and reliability growth
 - Learning curves
 - Flight duration across various aircraft types
- Uncertain policies
 - Export controls
 - Ground notification requirements
 - Alarm response
- Deployment timeframe

LCC Estimate Risk Mitigation

Summit Engineering Group role was to ...

- Develop comprehensive Cost Ground Rules and Assumptions
 - Promulgated and updated at each major program milestone
- Interface with major air carriers to discuss and socialize program assumptions
- Conduct intensive research into US commercial flight demographics
- Interface with vendors on developing detailed Manufacturing Rate Assessments



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Key Assumptions

- Quantity of CM Systems and Aircraft Modified
- Production start & initial deployment in FY08
- 20-year service life
- 2-level maintenance (Airport and OEM/Depot)
- Flights demographics
 - 350 Days per Year
 - Narrow body (NB), ~5 flights/ day, ~2.3 hours/ flight
 - Wide body (WB), ~2 flights/ day, ~6.8 hours/ flight
- \$2.00/gallon (BY03) applied to CM system induced fuel consumption
- >525 A-kit installs/ year could a ‘special visit’ penalty

–Illustrative–

LCC Estimate – Summary

LCC Phase	% of Total Cost
1. RDT&E	1.5%
2. Production & Deployment	23.4%
3. O&S	73.9%
4. De-Mod & Disposal	1.1%
Total	100.0%

Large Cost Drivers



- RDT&E – FY08 to FY18
- Production & Deployment – FY08 to FY17
- O&S – FY08 to FY34
- De-mod & Disposal – FY27 to FY35



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

–Illustrative–

LCC Estimate – RDT&E Phase

WBS Element	Phase%	LCC%
1.1 PMP	17.4%	0.3%
1.2 A/C Integr	0.0%	0.0%
1.3 Grd Sys Imp	0.0%	0.0%
1.4 ST&E	56.2%	0.8%
1.5 SE/PM	14.9%	0.2%
1.6 Support	1.1%	0.0%
1.7 Data	1.1%	0.0%
1.8 ECP	4.5%	0.1%
1.9 OGC	4.8%	0.1%
Total	100.0%	1.5%

- 73.6% of Total RDT&E \$ is for PMP and ST&E (shaded areas)
- Prime Mission Product (PMP)
 - ~LOE/Yr for Block Design Upgrades
- System Test & Evaluation (ST&E)
 - Periodic DT&E/OT&E to Support PMP block upgrades
 - LOE/Test Cycle & Test Materials
 - New/Amendment STCs each vendor
 - X quantity New STC
 - Y quantity Amendment STC

Strongest Influences or Highest Risk

- PMP – Extent of future design updates
- ST&E – # and Extent of STCs



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

–Illustrative–

LCC Estimate – Production/Deployment Phase

WBS Element	Phase%	LCC%
2.1 PMP	61.8%	14.5%
2.2 A/C Integr	3.6%	0.8%
2.3 Grd Sys Imp	0.0%	0.0%
2.4 ST&E	0.0%	0.0%
2.5 SE/PM	8.3%	2.0%
2.6 Supportability	20.3%	4.7%
2.7 Data	1.2%	0.3%
2.8 ECP	1.9%	0.4%
2.9 OGC	2.9%	0.7%
Total	100.0%	23.4%

- **85.7% of Production/Deployment \$ is for PMP, A/C Integration and Supportability** (shaded areas)
- **Prime Mission Product (PMP)**
 - Detailed T_1 (Labor/Mat'l) and Learning Curve across Each LRU
- **Aircraft (A/C) Integration**
 - Assumed no Learning for Modification/Install Labor based on numerous organizations performing them across time
- **Supportability**
 - Manufacturing Rate Assessment: Special Tooling/Prod Rate SE/Repair Station SE
 - Annual Quantity drives demand

Strongest Influences or Highest Risk

- **PMP – Assumed learning curve**
- **A/C Integration & Supportability – System deployment qty/rate**

Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

LCC Estimate – Operations & Support Phase

WBS Element	Phase%	LCC%
3.1 Mission Per	3.2%	2.4%
3.2 UL Consmpt	56.1%	41.4%
3.3 I/M Maint	16.1%	11.9%
3.4 Depot Maint	8.9%	6.6%
3.5 Ktr Support	3.5%	2.6%
3.6 Sustain Spt	8.8%	6.5%
3.7 Indirect Spt	1.4%	1.0%
3.8 ECP	0.5%	0.4%
3.9 OGC	1.5%	1.1%
Total	100.0%	73.9%

- 81.1% of Total O&S \$ is for Unit Level Consumption, Inter. Maint. and Depot Maint. (shaded areas)
- Unit Level (UL) Consumption
 - CM System induced Weight/Drag Impacts on Fuel Use across Aircraft Types (done for every discrete aircraft type) *Ex of how risk/uncertainty reduced*
- Intermediate Maintenance (I/M)
 - Unscheduled Repairs—due to MFHBF/year across each LRU—times \$/Repair
- Depot Maintenance
 - Periodic CM System Tech Refresh

Strongest Influences or Highest Risk

- Unit Level Consumption – Assumed fuel cost, induced drag
- Maintenance – System reliability



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

–Illustrative–

LCC Estimate – De-Mod/Disposal Phase

WBS Element	Phase%	LCC%
4.1 De-Mod	72.2%	0.8%
4.2 Disposal	27.8%	0.3%
Total	100.0%	1.1%

- De-Modification
 - Final removal of the Aircraft Modifications (e.g., A-kit)
 - 100% of original install time
 - Final removal of CM Equipment (e.g., B-kit)
 - 50% of original install time
- Disposal
 - All disposal costs of A-kit and B-kit material

Strongest Influences or Highest Risk

- De-Modification – % of labor effort from original installation



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

LCC Estimate – Sensitivities

Attribute	+ / - %	Low	LCC	High
\$/STC (New/Amend)	20	0.998	1.000	1.002
CM System T ₁	15	0.952	1.000	1.048
CM System Learning Curve	5	0.852	1.000	1.255
Fuel (\$/gal)	25	0.903	1.000	1.097
Fleet Drag (%)	20	0.941	1.000	1.059
Installed Weight (lbs)	10	0.991	1.000	1.009
Initial Reliability (MFHBF, WB/NB)	25	0.970	1.000	1.050
Order Quantity (For Illustrative Case)	5	0.958	1.000	1.040

- Costs normalized to ‘Base Case’
- Sensitivities are shown as being independent of each other
 - Correlations could result in significantly different impacts (e.g., an increase in fuel cost coupled with higher than projected drag effects)



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Risk Insights

- Highest Estimating Risk
 - System Deployment Quantity and Rate
 - Fuel Cost
 - System Reliability
 - Learning Curves
- Other ‘Influences’
 - NRE Cost for Each Aircraft Type
 - Technology Refresh Costs
 - Installation Weight (unless talking Regional Jets)
 - First Unit Cost (e.g., T_1)

Related Activities

- Deployment decision influenced by probability of threat and applicable cost/benefit analyses
- USC CREATE has done groundbreaking work on the economic impacts of a MANPADS attack
 - Avoiding the economic impact is a benefit
- Ongoing threat assessments are crucial to evaluating the likelihood of a MANPADS attack
- Metrics for quantifying the level of protection afforded by a given deployment alternative
 - More than just number of planes, number of flights, and/or number of passengers

Questions?



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.

Presenter Biographies

- Mr. Kurt Willstatter
 - Sr. Principal at Summit Engineering Group
 - Certified Cost Estimator/Cost Analyst (SCEA)
 - BA Biology (Texas A&M)
 - MS Operations Research (Naval Post Graduate School)
 - 15+ years of systems engineering, modeling & simulation, cost estimation experience
 - 20 years of Navy operations and systems engineering
- Mr. Richard “Andy” Campbell
 - Associate at Summit Engineering Group
 - Certified Cost Estimator/Cost Analyst (SCEA)
 - BS Mathematics, BA Economics (Rhodes College)
 - 4+ years of cost estimation, program analysis/management, and effectiveness modeling experience



Views, opinions, and/or findings contained in this briefing are those of the authors and should not be construed as an official Department of Homeland Security position, policy or decision unless so designated by other official documentation. No official endorsement should be inferred.
