



Defense, Space & Security
Lean-Agile Software

Satisfying DoD Contract Reporting With Agile Artifacts

Dick Carlson

richard.carlson2@boeing.com

SSTC 2011

Report Documentation Page

*Form Approved
OMB No. 0704-0188*

Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.

1. REPORT DATE MAY 2011	2. REPORT TYPE	3. DATES COVERED 00-00-2011 to 00-00-2011	
4. TITLE AND SUBTITLE Satisfying DoD Contract Reporting With Agile Artifacts		5a. CONTRACT NUMBER	
		5b. GRANT NUMBER	
		5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)		5d. PROJECT NUMBER	
		5e. TASK NUMBER	
		5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Boeing Defense, Space & Security, PO Box 516, St. Louis, MO, 63166		8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)		10. SPONSOR/MONITOR'S ACRONYM(S)	
		11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited			
13. SUPPLEMENTARY NOTES Presented at the 23rd Systems and Software Technology Conference (SSTC), 16-19 May 2011, Salt Lake City, UT. Sponsored in part by the USAF. U.S. Government or Federal Rights License			
14. ABSTRACT			
15. SUBJECT TERMS			
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT Same as Report (SAR)
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified	
19a. NAME OF RESPONSIBLE PERSON			

Environment

Boeing Defense, Space & Security | Lean-Agile Software

- MIL-STD-1521B, the FAR, and DFAR are based on waterfall life-cycle stages for technical reviews and contract reporting, and have specific contract metrics and reporting requirements
- “Agile concepts have been around for decades. In recent years, Agile matured and personnel became skilled in applying Agile; some DoD contractors started to build internal Agile capabilities and use Agile on DoD programs. Many DoD acquisition programs have also begun to propose and use Agile processes, attempting to take advantage of contractor capabilities; however, they have done this without (as yet) any formal DoD guidance, templates, or best practices.”

(Source: Considerations for Using Agile in DoD Acquisition, April 2010, SEI)

- How can proven Agile practices and principles be applied to projects that are not software-centric?
 - Boeing experience implementing Agile system engineering activities


Overview

Boeing Defense, Space & Security | Lean-Agile Software

- In the context of this presentation “Agile Systems Engineering” or AgileSE is limited to the definition and development of requirements for software systems
- We will identify specific systems engineering activities to which Agile was applied
- We will also include recommendations for applying Agile for project execution
- What will not be included is production relating to assembly and manufacturing and contractual impacts

Agile Practices Applied to SE “V” Model


Boeing Defense, Space & Security | Lean-Agile Software

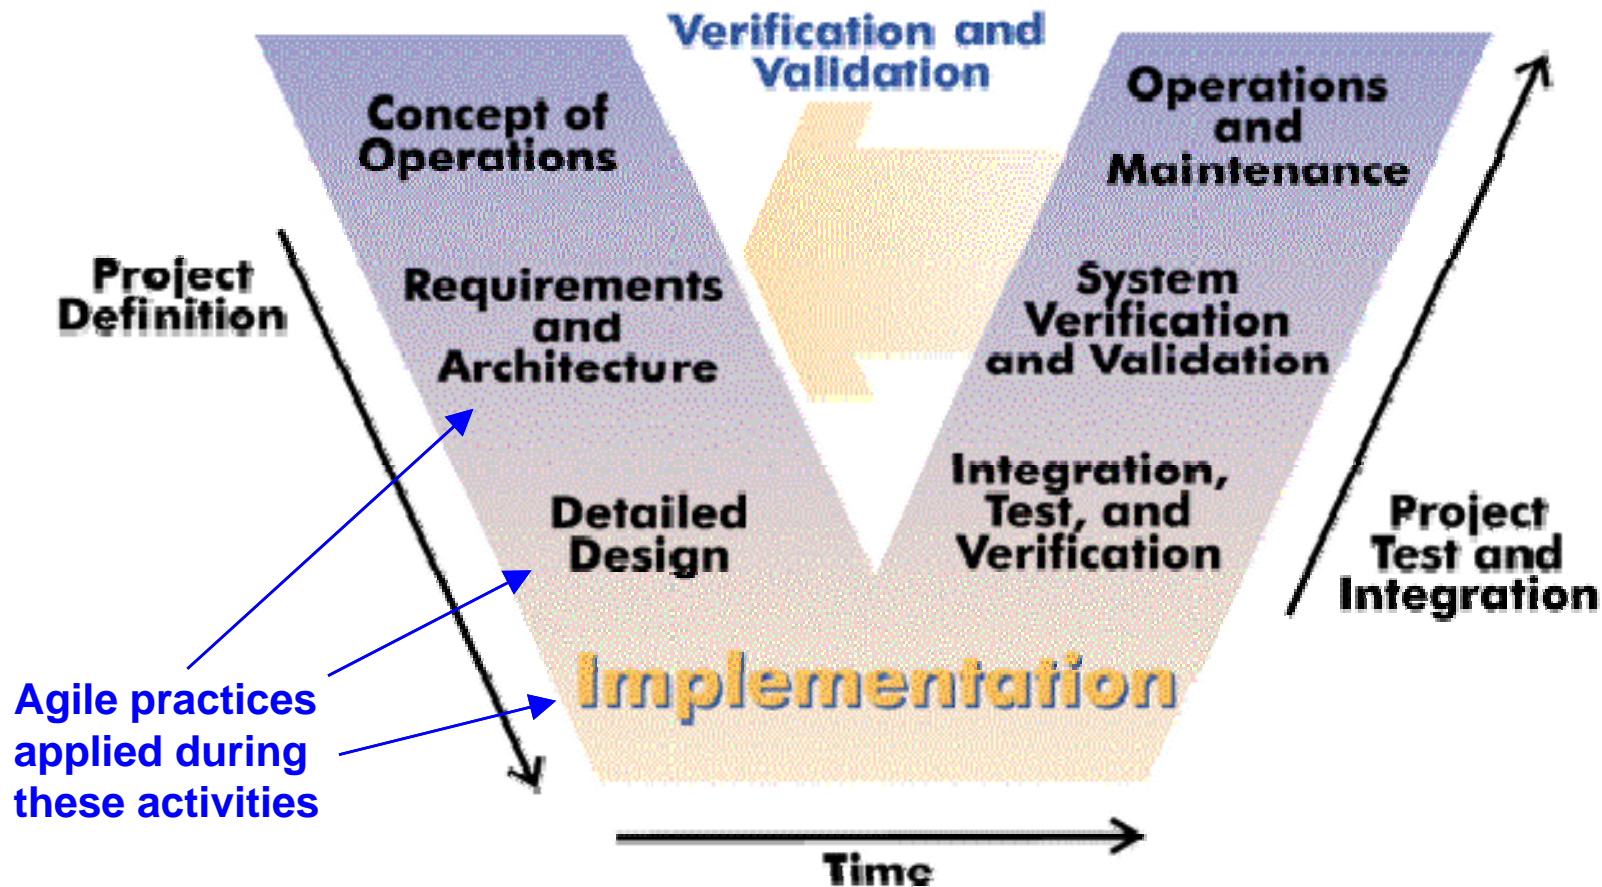

Source: <http://www.thefullwiki.org/V-Model>

Agile SE/SW Experience Model

Boeing Defense, Space & Security | Lean-Agile Software

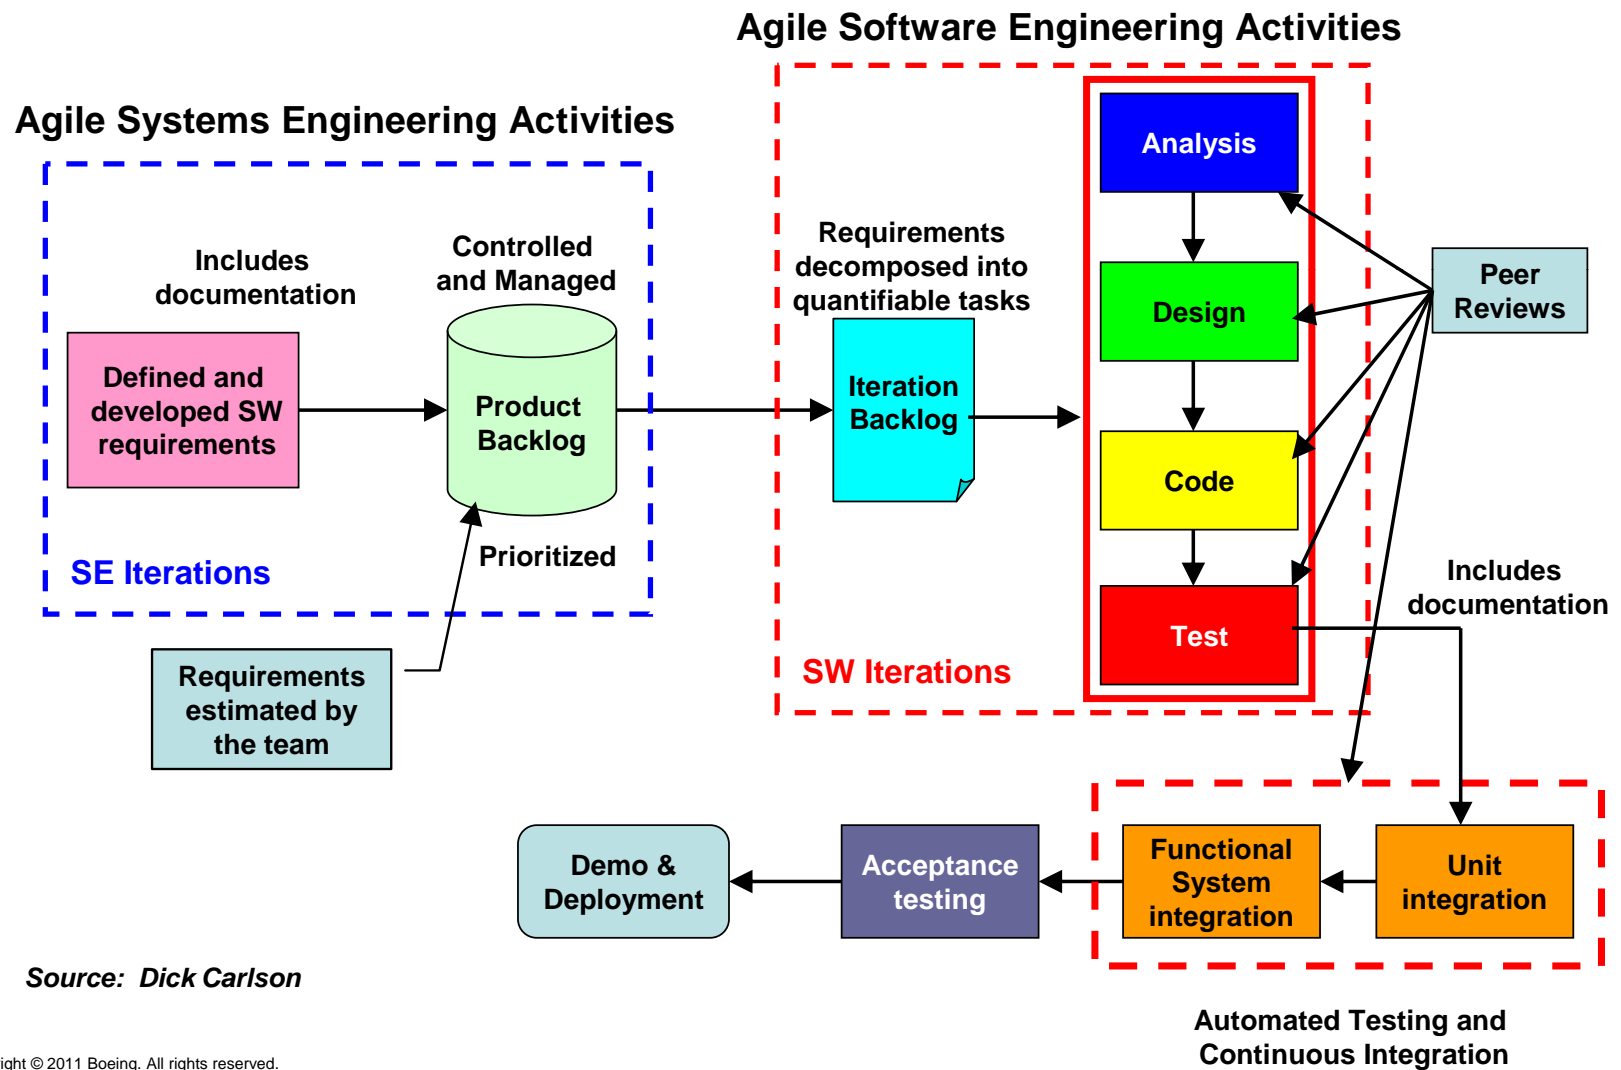

Source: Dick Carlson

Getting Started

Boeing Defense, Space & Security | Lean-Agile Software

- Conduct an assessment to determine if implementing Agile adds or reduces risk. For example:
 - Is the customer willing to actively participate, i.e. requirements clarification, product demos, incremental development?
 - Will there be regular and frequent customer communication?
 - Would the customer be willing to drive and prioritize requirements?
 - Is the customer willing to provide frequent feedback on items completed?
- If Agile can be applied with minimal risk, then train team in Agile
- Request an Agile coach be assigned to the project
- Focus more on planning than developing plans

Implement Simple Agile Practices

Boeing Defense, Space & Security | Lean-Agile Software

- Empower teams to self-manage and self-organize
- Close customer collaboration
- Daily stand-up meetings
- Planning and estimating
- Short iterations
- Prioritize requirements
- Artifact reviews – demonstrate functional prototypes

Prioritize Activities & Work Products

Boeing Defense, Space & Security | Lean-Agile Software

- Complete most important stuff first
- Lean out verbose documentation
- Defer architectural and design decisions until needed
- Verify all completed items
- Review completed items with key stakeholders

Establish a Vision


Boeing Defense, Space & Security | Lean-Agile Software

A vision that encourages and supports:

- Customer Satisfaction
- Frequent Delivery
- Motivated Team
- Working Software
- Technical Excellence
- Emergent Design
- Embracing Change
- Collaboration
- High Bandwidth
- Sustainable Pace
- Simplicity
- Continuous Improvement

Create a Project Roadmap

Boeing Defense, Space & Security | Lean-Agile Software

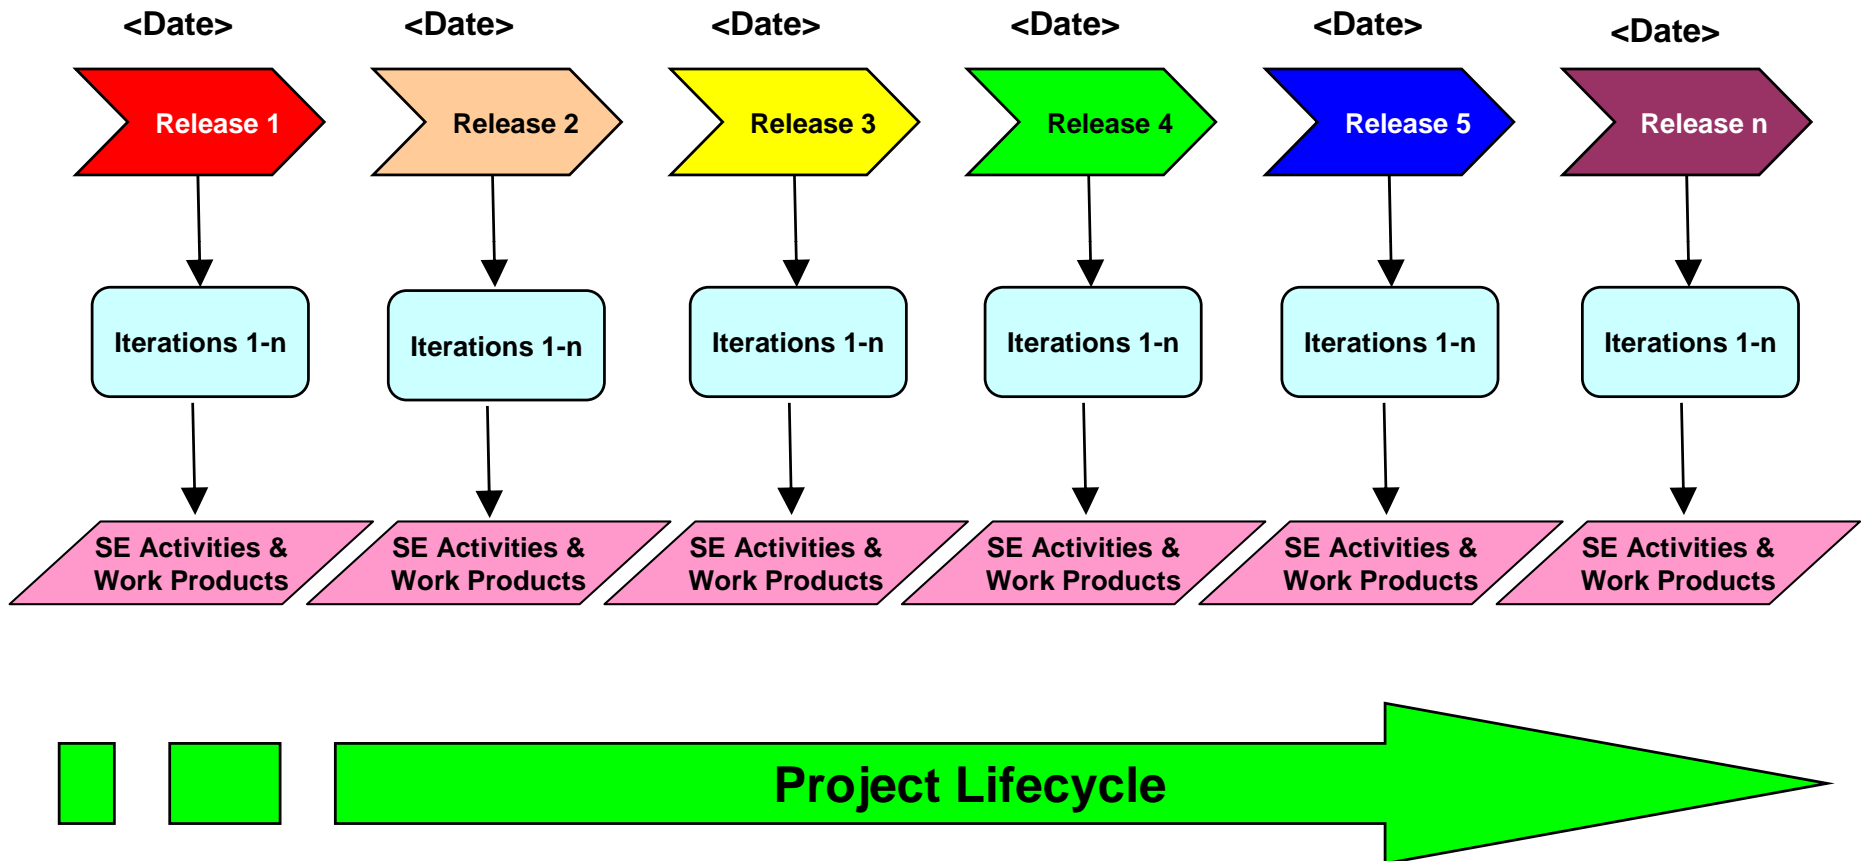

Source: Dick Carlson

Document Your Agile Approach

Boeing Defense, Space & Security | Lean-Agile Software

- Plan a release strategy through a series of short iterations to complete work products
- Use simple Agile modeling techniques
- Conduct daily standup meetings to identify previous work completed, what needs to be completed next, and any impediments
- Hold iteration reviews at the end of every iteration with key stakeholders
- Conduct team retrospectives to identify what worked well and improvement opportunities

Establish a Viable Release Plan

Boeing Defense, Space & Security | Lean-Agile Software

- Identify artifacts that will be developed incrementally
- Explain the importance of active customer involvement and feedback
- Elaborate through the project's Agile approach
- Obtain customer approval
- Distribute to everyone!
- Update often

Enlighten Your Customers



Boeing Defense, Space & Security | Lean-Agile Software

- Talk to them – let them know there is a viable alternative to the waterfall model (3 ways to do this)
 - Respond to a proposal need for Agile
 - Pre-proposal – recommend an Agile approach
 - Post-proposal – provide examples and show them how
- Identify the importance of their role in product development
- Train them on how to do this
- Get them to actively participate in the development validation process – their feedback is vital!
- Develop an accurate and meaningful release strategy

Meet Customers Half-Way

Boeing Defense, Space & Security | Lean-Agile Software

Project Milestone Reviews

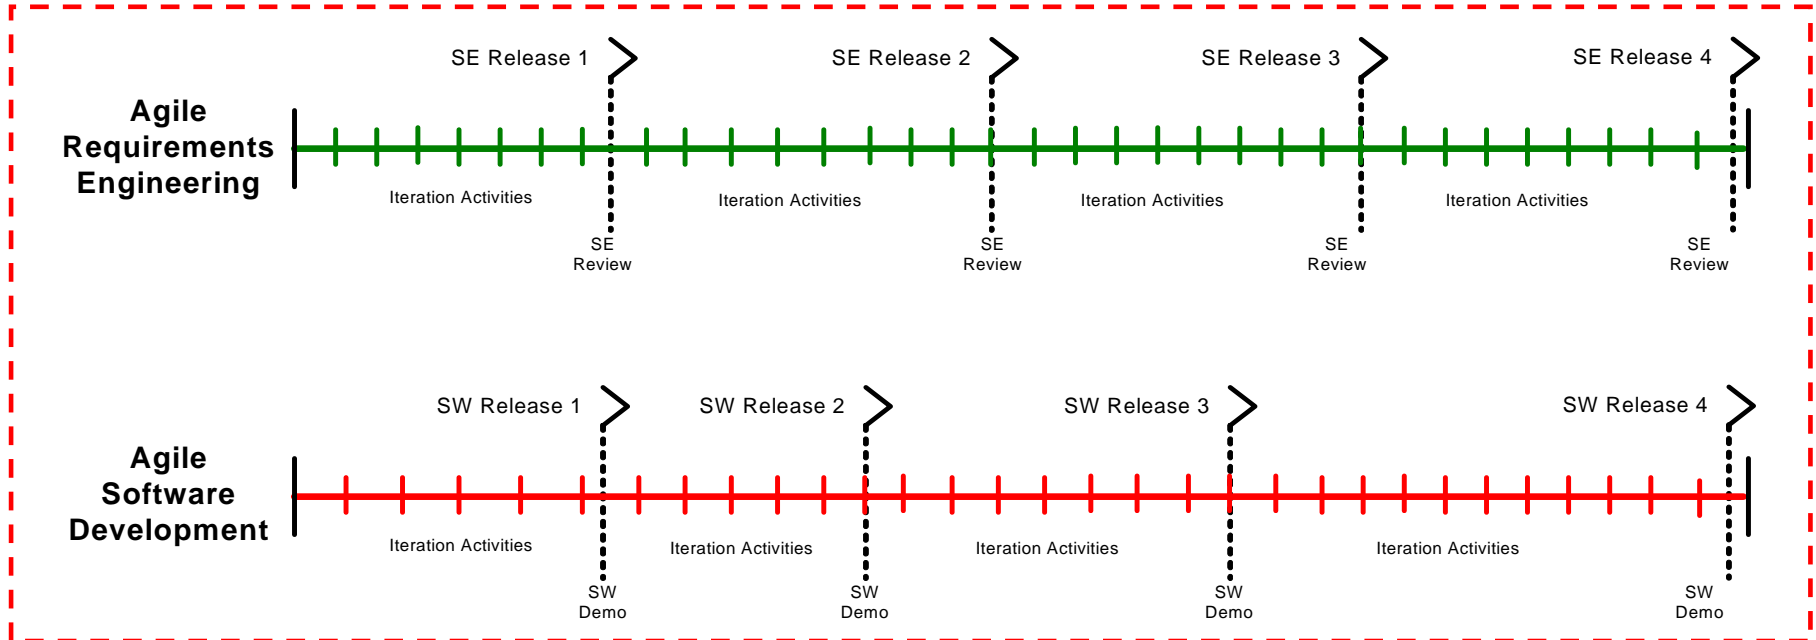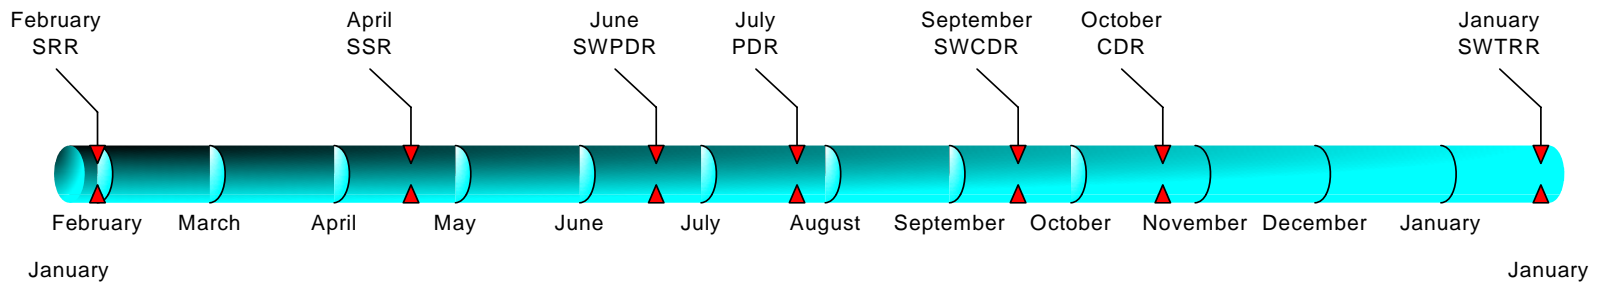

Make Everything Transparent

Boeing Defense, Space & Security | Lean-Agile Software

- Measure performance, productivity and quality
- Keep all work visible to everyone
- Announce all activities
- Celebrate successes!

Questions?

Thank You!

